COPY FOR LESSEE

MINING PLAN

(As Per MOEF & CC Notification No- S.0141 (E) Dated 15 January 2016 under Appendix XI)
With
Progressive Mine Closure Plan
Soil/Clay mining Project for

M/S SHIVAM INT UDYOG

Prop. Mr. Ram Ashish Gupta S/o Mr. Vanshi Gupta
Village: Balpur Srinagar Tarkulwa, District: Deoria. Uttar Pradesh.
Mining Site are at Gata No: 319, 49, 116, 96, 148.
Village: Alakhi Chappar, Jamuni Tappa, Balpur Srinagar, Tehsil: Deoria,
District: Deoria. Uttar Pradesh.

Mining Plan Period 5 Years (As Per Agreement), Total Area (1.513 ha.)

Mining plan submitted in DGM, Uttar Pradesh. For approval

PREPARED BY

M/S UDAIPUR MIN TECH PVT.LTD.

(QCI Accredited Consultant under NABET)
206, APEKSHA COMPLEX, HIRAN MAGRI, SECTOR – 11
UDAIPUR (RAJSTHAN)
RQP No. – RQP/UDP/354/2009/B, Valid upto 20.08.2019
Tel: 0522-2302662, 9616240230, 8563850701,
Email- udaipurminlko@gmail.com

(अनिल कुमार शर्मा)
ज्येष्ठ खान अधिकारी

Directorate of Geology and Mining, U
APPROVED
with condition vide letter
No. 6068 /MP/
04/8/18
DIREC

SUMMARY OF THE PLAN

1 - Name of the mineral- Brick Earth. M/S SHIVAM INT UDYOG

2- Name and location of Brick Kiln. Village: Balpur Srinagar Tarkulwa

District: Deoria, Uttar Pradesh.

3- Name and address of the Applicant.

Mr. Ram Ashish Gupta

S/o Mr. Vanshi Gupta

M/S SHIVAM INT UDYOG

Village: Balpur Srinagar Tarkulwa

District: Deoria.

Uttar Pradesh.

Proprietor/Partner of the Brick Kiln

4- Details of the Mining Area

a. District. Deoria

b. Tehsil. Deoria

c. Village. Alakhi Chappar, Jamuni Tappa, Balpur Srinagar

d. Gata No. 319, 49, 116, 96, 148.

e. Total Area (in hectare). (1.513 ha.)

5- Consent of the land owner. 5 Years

6- Period of the Mining Plan. 5 Years

7- Geological Reserve- 22,695 cu.meter / 27,234 Tonnes.

8- Mineable Reserve- 18,382.95 cu.meter/ 22,060 Tonnes.

9- Year Wise Production – 3,677 cu.meter/ 4,412 Tonnes.

M/s UDAIPUR MIN TECH PVT. LTD.
RQP/UDP/334/2009/B

LAND DETAILS

Gata no.	Village	Total area Ha.	Depth m	Period of agreement
319	Alakhi Chappar	0.676	1.5 Meter	5 Year
49	Jamuni Tappa	0.210	1.5 Meter	5 Year
116	Balpur Srinagar	0.174	1.5 Meter	5 Year
96	Balpur Srinagar	0.279	1.5 Meter	5 Year
148	Balpur Srinagar	0.174	1.5 Meter	5 Year
TOTAL		**1.513 Ha.**		

METHOD OF ESTIMATION OF RESERVE

Gata No.	Area In Ha.	Area in Sqm.	Excavated m Depth (m)	Area of Berm Left 10%	Volume of Berm Cu.m	Excavation Area Sqm.	Top Soil in cum	Reserve in cum	
								Geological Reserve	Mineable Reserve at depth
319	0.676	6760	1.5 Meter	676	1014	6084	912.6	10140	8213.4
49	0.210	2100	1.5 Meter	210	315	1890	283.5	3150	2551.5
116	0.174	1740	1.5 Meter	174	261	1566	234.9	2610	2114.1
96	0.279	2790	1.5 Meter	279	418.5	2511	376.65	4185	3389.85
148	0.174	1740	1.5 Meter	174	261	1566	234.9	2610	2114.1
TOTAL	**1.513 Ha.**	**15130 Sq.m.**		**1513 Sq.m.**	**2269.5 Cu.m.**	**13617 Sqm.**	**2042.55 Cu.m.**	**22695 Cu.m.**	**18382.95 Cu.m.**

M/s UDAIPUR MIN TECH PVT LTD
RQP/UDP/354/2009/B

खनन योजना तैयार करने हेतु
योग्य व्यक्ति के रूप में
मान्यता का प्रमाणपत्र

(खनिज रियायत नियमावली, 1960 के नियम 22(सी) के अंतर्गत)

M/s UDAIPUR MIN-TECH PVT. LTD.,

पंजीकरण संख्या-17-08522, पंजीकृत कार्यालय: 306-अपेक्षा कॉम्पलेक्स, सेक्टर नं.11, चौराहा एवं जिला-उदयपुर (राज), द्वारा अपनी योग्यताओं और अनुभव का संतोषप्रद प्रमाण प्रस्तुत करने के फलस्वरूप खनिज रियायत नियमावली, 1960 के नियम 22 (सी) के अंतर्गत उन्हें एतद्द्वारा खनन योजना तैयार करने हेतु योग्य संस्था के रूप में मान्यता प्रदान की जाती है.

उनका पंजीयन क्रमांक **आर.क्यू.पी./उदय/ 354/2009/B** है.

यह मान्यता दिनांक **20-08-2019** को समाप्त होने वाली दस वर्षों की अवधि के लिये वैध है.

स्थान : उदयपुर
दिनांक : 21.08.2009

(एस.टी.सावरकुडे)
क्षेत्रीय खान नियंत्रक
Regional Controller of Mines
भारतीय खान ब्यूरो
Indian Bureau of Mines
उदयपुर
UDAIPUR

सम्बद्ध व्यावसायिक प्रमुख व्यक्ति :-
1. श्री शैलेन्द्र सिंह बिष्ट पुत्र श्री बलवंत सिंह बिष्ट
2. डा.हरपाल सिंह यादव पुत्र श्री एल.एस.यादव

(एस.टी.सावरकुडे)
क्षेत्रीय खान नियंत्रक
भारतीय खान ब्यूरो

दिनांक 15.02.2010 से सम्बद्ध व्यक्ति (Key person) :-

1. श्री शैलेन्द्र सिंह बिष्ट, पुत्र श्री बलवंत सिंह बिष्ट
2. डॉ. हरपाल सिंह यादव, पुत्र श्री एल.एस.यादव
3. श्री [illegible], पुत्र श्री [illegible]

[illegible] 19/2/10
क्षेत्रीय खान नियंत्रक
भारतीय खान ब्यूरो
क्षेत्रीय खान नियंत्रक
Regional Controller of Mines
भारतीय खान ब्यूरो
Indian Bureau of Mines
उदयपुर
UDAIPUR

दिनांक 5-10-2012 से सम्बद्ध व्यक्ति (Key person) :-
1. श्री शैलेन्द्र सिंह बिष्ट, पुत्र श्री बलवंत सिंह बिष्ट - 5/10/2012
2. डा. हरपालसिंह यादव, पुत्र श्री एल.एस.यादव
3. श्री जैक लाल मेड, पुत्र श्री किशोरी लाल मेड

CERTIFICATE

We, M/s Udaipur Min-Tech Pvt. Ltd. hereby certify that

1. "The provisions of Mineral Conservation and Development Rules, 1988 have been observed in the Mining plan for Ordinary Soil Area Khasra No. 319, 49, 116, 96, 148. Over an area of 1.513 ha. for mineral Ordinary Soil in village: Alakhi Chappar, Jamuni Tappa, Balpur Srinagar, Tehsil: Deoria, District: Deoria, State: Uttar Pradesh belonging to **M/S SHIVAM INT UDYOG** Prop. Mr. Ram Ashish Gupta, Village: Balpur Srinagar Tarkulwa, District: Deoria. State Uttar Pradesh and wherever specific permission is required the applicant will approach the concerned authorities of Department of Mines & Geology for granting the permission."

2. It is also certified that the provisions of Mines Act, Rules and Regulations made there under have been observed in the aforesaid Mining Plan and wherever specific permissions are required the applicant will approach the Director General of Mines Safety.

3. It is further certified that the aforesaid Mining Plan is prepared as per the copies of the records and documents provided by applicant and information given as per discussions held with applicant and his representative.

4. It is also certified that the information furnished in the aforesaid Mining Plan are true and correct to the best of our knowledge & belief and in case of default the approval would be withdrawn.

For M/s Udaipur Min-Tech Pvt.Ltd

(RQP/UDP/354/2009/B,Valid up to 20.8.2019)

MINING PLAN

1.0 GENERAL INFORMATION ABOUT PROJECT PROPONENT

1.1 Name and Address of Project Proponent

Mr. Ram Ashish Gupta

S/o Mr. Vanshi Gupta

M/S SHIVAM INT UDYOG

Village: Balpur Srinagar Tarkulwa

District: Deoria.

Uttar Pradesh.

1.2 STATUS OF PROJECT PROPONENT

The Project Proponent is private individual involved in manufacturing the bricks.

1.3 MINERAL / MINERALS WHICH THE PROJECT PROPONENT INTENDS TO MINE

The project proponent has applied for mining the brick clay to manufacture kuccha bricks to be used further in brick kiln.

1.4 NAME, ADDRESS AND REGISTRATION NUMBER OF THE QCI CONSULTANT & RQP

M/S UDAIPUR MIN TECH PVT.LTD.

(QCI Accredited Consultant under NABET)

RQP No. – RQP/UDP/354/2009/B,

Valid upto 20.08.2019

Tel: +91, 9616240230, 8563850701,

Email- udaipurminlko@gmail.com

2.5 SOCIAL INFRASTRUCTURE

2.5.1 Road- The nearest SH. 79 Deoria- Kushinagar road at an aerial distance of 0.8 km in East direction from project site.

2.5.2 Water- Water for drinking provided by hand pump from nearby Area. Additionally a water tank will be provided for mining activity.

2.5.3 Electricity- All the Villagers in and around 5 km radius are electrified.

2.5.4 Education-Nearest Tarkulwa Primary School at an aerial distance of 1.5 Km. in South direction.

2.5.5 Hospital- Nearest District hospital Deoria are at an aerial distance of 18.0 Km. in South-West direction.

2.5.6 Railway Station- Nearest railway station is the Deoria near about 18.0 Km. in South- West direction.

2.5.7 City/Town- Nearest town is the Tarkulwa at an aerial distance of 1.5 Km. in South direction.

3.0 GEOLOGY AND RESERVE

3.1 TYPE OF PROJECT

This is an independent brick clay project. The proposed project is for the extraction of brick clay form the allotted plot(s) manually.

Location (Map Showing General Location and Project Boundary and Project Site) with COORDINATES

The mining lease area is located at Plot No. 319, 49, 116, 96, 148. Village: Alakhi Chappar, Jamuni Tappa, Balpur Srinagar, Tehsil: Deoria, District – Deoria. Uttar Pradesh. The proposed project activity will be carried out in the allotted plot(s). Google map 5 km radius is showing project location of plot(s) to be excavated is attached as Annexure 1 respectively.

VILLAGE	LATITUDE	LONGITUDE
ALAKHI CHAPPAR	26°38’39.16” N	83°54’11.19” E
JAMUNI TAPPA	26°38’21.97” N	83°54’22.26” E
BALPUR SRINAGAR	26°38’22.30” N	83°53’23.10” E

3.2 PHYSIOGRAPHY

This district is located between 26 degree & 28 degree north latitude and 83 degree & 85 degree east longitude out of which district Kushinagar was created in 1994 by taking north & east portion of Deoria district. District deoria is surrounded by district kushinagar in North, district Gopalganj & Siwan (Bihar state) in East, district Mau & district Ballia in south and district Gorakhpur in West. Deoria district headquarter is situated at 53 km. milestone from Gorakhpur by road towards east. District headquarter is situated at 50 km from Gorakhpur on Gorakhpur-Siwan broadgauge railway line towards Siwan. Ghaghara, Rapti & Chhoti Gandak are the main rivers in this district. Besides these, Gorra, Bathua, Kurna, Majhne, Nakta are small river/nala which originate from above mentioned rivers.

Climate of the district is 'SAMSITOSN' .May & June are hot and December & January months of the year are cold. Soil of different types is found in the district. Domat, Bhat, Matiyar & Balui Domat is found commonly. Productive & densely populated this district of Uttar Pradesh is situated at the north-east end of the state. Currently, Deoria district has five tehsils namely Deoria sadar , Deoria, Rudrapur , Berhaj & Bhatparrani Geomorphologically the district can be grouped into three geomorphic units as detailed below:

1. Recent flood plain of stream - Yellow colored clay, silt and sand of various grades.
2. Terrace Zone - Yellow and grey colored silt, sand and kankar beds.
3. Older Alluvial Plains - yellow grey colored silt, sand and kankar beds.

3.3 TOPOGRAPHY

Topographically, the area is almost open plain, sloping gently from north to south in the western side & North West to west in the eastern side. The highest elevation of the district is 195.072 m above msl and the lowest is 173.76 m above msl. The average gradient of land surface is 2 cm/km

3.4 GEOMORPHOLOGY & SOIL

The district consist Major soil types are Bhur, Matiyar & Domat. The Ganga Yamuna Doab region is a riverine region endowed with fertile soil, favorable climate, flat surface and slow moving river. This region with its deep, fertile, stone less, alluvial soil and its many rivers is the most favorable and most desirable part of India. The project site area is lies in the Ganga Khadar Region.

fore deep between Plateau region in south and Himalayas in north during the Quaternary period by the Indus-Ganga system of drainage over the Precambrian topography existing during geological past. These deposits owe their origin to riverine activity. The southern part of the State has entirely different geological conditions being underlain by Precambrian formations under a thin alluvial cover. Broadly, the State can be divided into two hydro geological units.

1. Unconsolidated zone. 2. Consolidated, hard rock zone. The project site area lies into the unconsolidated zone.

Unconsolidated Zone: The unconsolidated formations comprising the area have been deposited through mighty rivers originating from great Himalayan Mountains. These sediments are an admixture of pebble, gravel, sand, silt, clay and kankar. The sediments are generally coarser in the north and gradually become finer south east ward along downstream of the drainage which is a typical feature of fluvial deposits. This zone consists of mainly two parts, the Terai and the Alluvial Plain. However, foot hill zone is very small part of Bhaber belt and lies in the northern parts of Deoria and Saharanpur districts. The Terai is a narrow disconnected belt along the north western fringe of the State. The Alluvial Plain occupies the area south of Terai and can further be divided in two sub units - Younger Alluvium and Older Alluvium. The younger alluvium occurs mostly along the present day flood plain area. The continuous shifting of the drainage network with time caused reworking of their earlier deposits giving rise to the younger alluvium. The older alluvium occupying comparatively high area covers major part of the Plain. A typical characteristic of older alluvium is formation of kankar within itself due to leaching of calcium carbonate under favorable climatic conditions. The kankar occasionally forms pans restricting downward movement of water.

3.8 LOCAL GEOLOGY

Deoria district falling in Central Ganga Plain lies in inter fluvial tract of Ganga and Yamuna. Hydro geological data indicates that the area is underlain by moderately thick pile of quaternary sediments, which comprises of sand of various grades clays & kankar. Alluvial sediments overlies Vindhyan group of rocks in an unconformable way. Thickness of deposits varies from 287 to 380 meters.

3.9 HYDROGEOLOGY

Ground water occurs in the pore spaces of unconsolidated alluvial material in the zone of saturation. In Deoria district ground water occurs under water table conditions at shallow depths while in deeper aquifer are under confined state of disposition, the confining layers are impermeable clay beds. The pre monsoon depth to water map prepared on the basis of National Hydrograph Stations and State Government Wells reveals that depth to water ranges between 2.06 and 21.00 meters. Shallow water level conditions between 5-10 metres occur along the Upper Ganga Canal. Deepest water level more than 15 meters has been observed in the central part of the district. Rest of the area water level occurs between 10-15 mbgl. Perusal of post-monsoon map reveals that water level in post monsoon period generally ranges between 1.96 and 17.00 meters below ground level less than 5 meters (shallow) water level occurs in the eastern & western part along Ganga and Yamuna rivers & along the main canals and their distributaries. Shallowest water level of 1.96 mbgl was observed near the Upper Ganga Canal.

LITHOLOGY

No rock unit is exposed in the area applied for proposed project.

STRUCTURE

Not applicable in absence of rock unit.

NATURE OF MINERALIZATION

Not applicable in absence of rock unit.

EFFECT OF WEATHERING

Not applicable in absence of rock unit.

NATURE OF WALL ROCKS

Not applicable in absence of rock unit.

PHYSICAL CHARACTERISTICS

The brick earth is light brownish. The brick earth is suitable for making the bricks.

3.10 DETAILS OF EXPLORATION

(A) Already Carried Out in the Area

No pit is observed in the area.

(B) Proposed to be Carried Out

Brick Earth is available on the surface, thus prospecting is not needed.

3.11 METHOD OF ESTIMATION OF RESERVES

The reserves are calculated by the following formula

Volume of earth = excavable area * depth of Mine

Brick earth in tonnes = Volume of Brick earth * bulk density.

The bulk density of the brick earth is 1.2 tonnes per cum.

Probable category reserves= Total around 1.513 hectares area.

Volume of Brick Earth.

Gata No.	Area In Ha.	Area in Sqm.	Excavated m Depth (m)	Area of Berm Left 10%	Volume of Berm Cu.m	Excavation Area Sqm.	Top Soil in cum	Reserve in cum	
								Geological Reserve	Mineable Reserve at depth
319	0.676	6760	1.5 Meter	676	1014	6084	912.6	10140	8213.4
49	0.210	2100	1.5 Meter	210	315	1890	283.5	3150	2551.5
116	0.174	1740	1.5 Meter	174	261	1566	234.9	2610	2114.1
96	0.279	2790	1.5 Meter	279	418.5	2511	376.65	4185	3389.85
148	0.174	1740	1.5 Meter	174	261	1566	234.9	2610	2114.1
TOTAL	**1.513 Ha.**	**15130 Sq.m.**		**1513 Sq.m.**	**2269.5 Cu.m.**	**13617 Sqm.**	**2042.55 Cu.m.**	**22695 Cu.m.**	**18382.95 Cu.m.**

BRICK EARTH IN TONNES = 18,382.95 *1.2
= 22,060 Tonnes

4.0 METHOD OF MINING

This is an open cast Mining. The excavation of Brick Earth will be done by Semi- Mechanized **(With the help of Excavator)** be used during excavation period. The Brick Earth required per year will be around 4,412 tonnes.

OTHERS

a. The approach road will be smooth and wide.

b. Plantation will be done in near and around the proposed area during monsoon. Tree and separate watering arrangements will be provided.

c. Personal protective equipments like safety helmet, safety shoes, safety goggles. Dus. respirators will be provided to the laborers as work requirement.

d. Drains with parapet walls will be provided around the pit to check the entry of flowing monsoon water in the pit.

e. Fencing will be done around the excavation to check the inadvertent entry of human and live stock is the mining zone.

4.1 DEVELOPMENT PROPOSED FOR THE PERIOD OF THE PROJECT

First Year:-

From the MLA 4,412 TPA Brick earth will be excavated from the area for achieving a production of Approximately 18.38 lacs bricks per Year.

Second Year:-

From the MLA 4,412 TPA Brick earth will be excavated from the area for achieving a production of Approximately 18.38 lacs bricks per Year.

Third Year:-

From the MLA 4,412 TPA Brick earth will be excavated from the area for achieving a production of Approximately 18.38 lacs bricks per Year.

Forth Year:-

From the MLA 4,412 TPA Brick earth will be excavated from the area for achieving a production of Approximately 18.38 lacs bricks per Year.

Fifth Year:-

From the MLA 4,412 TPA Brick earth will be excavated from the area for achieving a production of Approximately 18.38 lacs bricks per Year.

YEAR	CU.M. PER YEAR	TONNES PER YEAR
FIRST	3,677	4,412
SECOND	3,677	4,412
THIRD	3,677	4,412
FORTH	3,677	4,412

FIFTH	3,677	4,412

In case Brick Earth is fully exploited in the area and further no more Brick Earth is available, applicant will separately apply for other land and Mine Plan will be prepared accordingly.

4.2 PROPOSED RATE OF PRODUCTION

During the period of the project the required production of Brick Earth is around 4,412 tonnes. Per year.

4.3 RESERVES OF BRICK EARTH USED DURING THE PERIOD OF THE PROJECT IN AREA.

As per paragraph 3.3 the mineable reserve of Brick Earth is 22,060 tonnes. Around 4,412 tonnes. of brick earth will be excavated during the Five Years of the proposed period. Thus the reserves are quite sufficient for the period of Five years. In case Brick Earth is fully exploited in the area and further no more Brick Earth is available, applicant will separately apply for other land and Mine plan will be prepared accordingly. Mine Plan will be prepared accordingly.

4.4 METHOD OF MINING

The mining i.e. excavation of Brick Earth is by Semi Mechanized **(With the help of Excavator)** of opencast mining. The length and depth of the road will depend on the depth of excavation. The excavation of Brick Earth will be by simple hand tools. Around 25 tonnes of Brick Earth has to be excavated and loaded per day considering 180 days of effective working after deduction of monsoon period and other holidays.

For transportation of casted bricks from proposed site to kiln, one wheel wooden cart will be Utilized.

4.5 PREPARATION OF KUCHCHA BRICK.

Pasar: The place where Brick Earth is mixed with water for molding.

Mould: Wooden4ron mould of average 9" x 4.5" x 3" Size is used for making the kuchcha brick. Prepared clay will be poured in the mould and pressed manually, than mould will be removed leaving kuchcha brick.

Sun Drying: The kuchcha brick will be allowed for sun drying. This is an important step for making the adobe (kuchchi brick). The final moisture content of the adobe brick remains around 10% to 15%.

Transportation: The kuchcha bricks transported from drying place to brick kiln chamber by one Wheel hand operated cart. This cart transports around 30 to 40 bricks at a time.

SITE SPECIFICATION

i. Site Office: The site office with all requisite facilities is available at site.

ii. Water Huts: Water huts are available at requisite sites.

iii. Latrine & Bathrooms: This facility is mobile and available at site.

iv. Staff Quarters: Available at site.

v. Rest Shelters: The rest shelter for laborers is available just nearby the site.

vi. Other: Temporary site services will be provided as advised by the officials time to time.

4.6 EMPLOYMENT POTENTIAL

Almost 38 unskilled labours will be deployed in brick clay mining.

4.7 SITE SERVICE

The workings will be for. The following site service is available at site:

1. Temporary toilet will remain available at site.
2. Migrants are not allowed as local resident will be employed.

4.8 CONCEPTUAL MINING PLAN

Conceptual mining plan is necessary to know the ultimate limit if the pit crust when whole reserves will be exhausted. The ultimate pit Limit is limit of pit surface at the end of mining. It is also necessary to select the sites for waste dump, site service, plantation etc. in such a place that these sites should not get any disturbance during the life of the mine. Considering the aforesaid aspects the conceptual mining plan is proposed as follows:

A) Ultimate Extent & Size of the Pit(s)

Gata no.	Village	Total area Ha.	Depth m	Period of agreement
319	Alakhi Chappar	0.676	1.5 Meter	5 Year
49	Jamuni Tappa	0.210	1.5 Meter	5 Year
116	Balpur Srinagar	0.174	1.5 Meter	5 Year
96	Balpur Srinagar	0.279	1.5 Meter	5 Year
148	Balpur Srinagar	0.174	1.5 Meter	5 Year
TOTAL		**1.513 Ha.**		

B) THE FINAL SLOPE ANGLE ADOPTED

Considering final slope angle will be 45°.

C) ULTIMATE CAPACITY OF DUMPS

The dumps are not required as whole earth is useable.

D) STABILIZATION OF DUMPS

There will be no waste generate in brick earth mining. The excavated brick earth will be used for manufacture of kuchcha bricks.

E) ULTIMATE PIT LIMIT

It is a Brick Clay Mining project and the ultimate pit limit is the boundary of 1.513Hectare land with its safety margin as per the closure plan.

5.0 DRAINAGE

General ground level in nearby area of project is 77 mRL whereas level of ground water table is Around 10 m below from general ground level. This level fluctuates around 3 meters in dry and wet season. Proposed deepest working will be around 1.5 meters deep. Thus ground water table will not be affected adversely.

DEWATERING

During the monsoon, the rain water will collect in the pit. This water will percolate in ground containing brick Earth. Thus dewatering is not required. Rain Water will be used in proposed plantation.

PLANTATION

Existing: Presently no big tree is observed in the proposed area. The seasonal shrubs and bushes are observed in the nearby area.

Proposed: Around 250 trees will be planted in nearby area and around the proposed area and Between tar road and proposed area. Proper protection devices for survival of trees will be provided. The separate watering arrangement will be provided.

The trees will be planted between the road and applied lease area and along the lease boundary and approach road. The dead plants will be replaced by fresh plants in next monsoon.

YEAR.	NO. OF SAPLING	SPECIES	PLACES OF PLANTATION
FIRST	50	GIVEN BELOW	Around Road side & Gram Panchayat Land
SECOND	50	GIVEN BELOW	Around Road side & Gram Panchayat Land
THIRD	50	GIVEN BELOW	Around Road side & Gram Panchayat Land
FOURTH	50	GIVEN BELOW	Around Road side & Gram Panchayat Land
FIFTH	50	GIVEN BELOW	Around Road side & Gram Panchayat Land

The proposed plants are as follows

The plantation should be grown in each monsoon.

The tree guards and proper watering arrangements will be provided for achieving the good survival rate.

S.NO.	BATANICLA NAMES	HINDI NAMES
1.	Syzygium cumin	Jamun
2.	Emblica officiaalis	Awala
3.	Ficus glomerata	Gular
4.	Azadirachta indica	Neem
5.	Dalbergia sisso	Shisham
6.	Cassia fistuala	Amaltas

10.0 MEASURE TAKEN AND TO BE TAKEN FOR PROTECTION OF ENVIRONMENT IN AND AROUND THE LEASE AREA

Existing

Present environment and aesthetic beauty of the area is good.

Proposed

Due to mining the level of the surface will lowered 1.5 meters. No waste will generate. No tree will destroy by proposed mining activities. For protection of environment and improving the aesthetic beauty of the area following measures will be provided:

The mining will be systematic and scientific in supervision of technical staff.

S. NO.	CATEGORY	PROPOSED LAND USE (HA.)
1.	Quarry Area	1.362
2.	Waste Dump	0.000
3.	Top Soil Dump	0.026
4.	Road Area	0.024
5.	Built up Area	0.021
6.	Processing Area	0.023
7.	Storage Area	0.020
8.	Plantation Area	0.018
9.	Undistributed Area	0.020
TOTAL MINING AREA		**1.513 ha.**

Flora

The Deoria district covered mixed variety of vegetation mainly buses. The tress like Shishum, Neem, Mango tree and Jamun tree, Eucalyptus and Babool are found in sufficient numbers.

Fauna

Fish: - Mahaser, Hilsa, Saul, Tengan, Parthan, Rasela, Vittal, Rohu, Mirgal,Kata, Labi, Mangur, Cuchia, Eel, Einghi, Mirror Carp, Trout.

Amphibia: - Frog and Toad.

Reptiles: - Bamania, Pit-viper,Lizard, Goh, Cobra,Tortoise, Krait, Dhaman and Crocodile.

Aves: - Cheel, Vulture, Peacock, Nightingale, Pigeon, Parrot, Owl, Nilkanth and Sparrow.

Mammals: - Shrew, Porcupine, Sqirrel, Hare, Mongoose, Cow, Buffalo and Mouse.

Other common species found here are Nilgai, goat, cow, buffalo, Elephant etc. Among the birds Fowl, Pheasant, Partridge, Florican, Duck, Goose and Wader are common.

CLIMATIC CONDITION

This district is located between 26 degree & 28 degree north latitude and 83 degree & 85 degree east longitude out of which district Kushinagar was created in 1994 by taking north & east portion of Deoria district. District deoria is surrounded by district kushinagar in North, district Gopalganj & Siwan (Bihar state)in East ,district Mau & district Ballia in south and district Gorakhpur in West. Deoria district headquarter is situated at 53 km. milestone from Gorakhpur by road towards east. District headquarter is situated at 50 km from Gorakhpur on Gorakhpur-Siwan broadgauge railway line towards Siwan. Ghaghara, Rapti & Chhoti Gandak are the main rivers in this district. Besides these, Gorra , Bathua , Kurna ,Majhne ,Nakta are small river/nala which originate from above mentioned rivers. Climate of the district is 'SAMSITOSN' .May & June are hot and December & January months of the year are cold. Soil of different types is found in the district. Domat , Bhat , Matiyar & Balui Domat is found commonly. Productive & densely populated this district of Uttar Pradesh is situated at the north-east end of the state. Currently,Deoria district has five tehsils namely Deoria sadar , Deoria, Rudrapur , Berhaj & Bhatparrani

HUMAN SETTLEMENTS

No human settlement observed in the applied area.

11.0 Measures Taken and to be taken for Dumping Overburden, Stacking of Top Brick Earth and Utilization of Top Brick Earth

In Brick Earth mining for brick kiln the maximum quantity of excavated Brick Earth will use in making the adobe bricks.

WASTE DUMP AND STABILIZATION

No waste will generate due to Brick Earth mining.

The bricks are sailable from full brick to crack bricks (pieces of bricks).

TOP BRICK EARTH

The mining will be for Brick Earth and the Brick Earth will use in manufacturing the bricks.

12.0 MEASURES TAKEN AND TO BE TAKEN FOR CONTROL OF WATER, NOISE AND AIR POLLUTION

General ground level in nearby area of project is 77 mRL whereas level of ground water table is Around 10 meters below from general ground level. This level fluctuates around 3 meters in dry and wet season. In dry season it lowered around 2 meters, proposed deepest working will be around 1.5 meters deep. Thus ground water will not come across.

DEWATERING

During monsoon the rain water of direct precipitation will collect in the working pits. The monsoon water of upper altitude side may also collect in the pit.

A drain will be provided around the pit to divert the rain water away from the pit.

The rain water come across during the monsoon, the rain water will collect in the pit. This water will percolate in Brick Earth.

The source of drinking water is tube well and hand pumps, which are away from the area and thus not get any adverse effect from mining.

NOISE

Approach roads within the premises of brick kiln area will be stabilized with brick bats/keri etc. The whole process is manual thus noise pollution will remain in permissible limit.

AIR POLLUTION

The roads within the area will be kept wide, smooth and properly wet by water spray.

Dust pollution Measures proposed

A. All the haul roads will be kept wide, leveled and compact.

Regular water Sprinklers should be done on road from site to tar road once or twice in a day especially during dry season to check the generation of dust during vehicular movement.

B. The green belt in and near the lease area will minimize dispersion of dust in nearby area. The

Proposed plantation is illustrated on the plan.

c. The proposed plantation along both sides of haul road from tar road and between tar road and mine site will also check the spread of dust in nearby area.

D. Monitoring in six month is proposed for assessment of impact for generation of dust due to vehicular movement, drilling, blasting and loading etc. and measures should be adopted to minimize the gaseous pollution.

PERSONAL PROTECTIVE EQUIPMENT

The safety helmet, safety shoos, safety belts will be provided to the laboures to the dust respirators will be provided to the workers who will work near the noise creating machines.

13.0 CONTRIBUTION REGARDING THE SOCIAL DEVELOPMENT OF THE NEARBY RESIDENTS

The socio-economic benefits can be maximized, if environmental concerns are integrated in planning during development of the project i.e., by eco-friendly mining. The environmental patterns likely to be affected are as follows:

There is no impact of mining on local residents of the area as habitation is away from the proposed area. The maximum persons will be employed from nearby villages. There is no source of employment in nearby area and thus the employment will develop by the proposed mining activity in nearby area. The villagers may use the wastage of bricks (not saleable) free of cost.

The impact of mining on social demographic profile is always positive, because all the persons have been employed from nearby villages. Apart from indirect employment, some persons get satellite occupation like tea stall, shops and small workshops due to mining activities in the area. Some persons will get occupation as transporter of pucka brick from site to consumers. Thus the mining has raised the economic status of nearby villagers.

The project Proponent will contribute some fund from the income and the fund will used only for the social development of the people in the field of Education and medical.

14.0 DETAILS OF HEALTH CHECKUP AND INSURANCE OF ALL THE EMPLOYED PERSONS (FOR EXISTING LEASE)

The health and safety hazards will be anticipated to affect the persons employed at the brick kiln. The persons may get injury by fall of bricks or may suffer from professional diseases while working at brick kilns. Safety boots and hats will be provided to the employed persons. A first-aid box is kept at the mine. The dispensary is located near by the area.

15.0 OTHERS

The approach road to site of brick kiln (including the storage site) from the nearest public road for the transportation of final products must be paved or hard surfaced.

Water storage facility (minimum 2.0 KLD) must be provided at the brick kiln site.

A Sign Board showing the name, address and capacity of the brick kiln industry should be displayed at the entrance of the site and on nearest road,

Dust respirators will be provided to the laborers.

16.0 FINANCIAL ASSURANCE

As per rule 37J (1) and (3) the applicant will submit the financial assurance of rupees 16000 / ha. In term of fixed deposit receipt from any scheduled Bank before issuing the sanction letter.

17.0 ENVIRONMENTAL PROTECTION

17.1 MINE CLOSURE PLAN

Before excavation of soil approximately 10% area of total land are leave for Berm. A depth of 0.15 meter of top soil form mining area is stored near the Berm area. After excavation of 1.5 meter soil from mining area the top soil is spread in the mining area and the land are hand over to the land owner. For the protection of soil degradation of nearby land fast growing species of sabai grasses are planted at the Berm area that bound the soil and prevent soil degradation.

17.2 WATER QUALITY MANAGEMENT

No surface water body located in the lease area. General ground level in nearby area of project is 77mRL whereas level of ground water table is around 10 meters below. This level fluctuates around 3 meters in dry and wet season. In dry season it lowered around 3 meter. Proposed deepest working wilt is around 1.5 meter deep. Thus ground water will not come across.

17.3 AIR QUALITY SURVEY

The magnitude of air pollution in mining is machineries with method of mining, type of mineral and level of mechanization. The Brick Earth is loose and thus blasting etc will not require. The source of air pollution will be excavation and loading of Brick Earth and transportation vehicle. The following measures will be provided:

1. Water spray will be provided over the Brick Earth before excavating. The spray will be in upper layers. In lower layer the Brick Earth comes across in wet form.
2. Water sprinklers will be provided on the kuchha approach road to minimize the dust during Vehicular movement.
3. The plantation along the kuchha approach road will also help to spread the dust outside.

17.4 WASTE MANAGEMENT

Not applicable in absence of waste.

17.5 TOP BRICK EARTH MANAGEMENT

The Brick earth will be excavated from the area thus no management will require.

17.6 TAILING DAM MANAGEMENT

No tailing dam is proposed hence this paragraph is not applicable.

17.7 INFRASTRUCTURE

No infrastructure is proposed at site for the proposed project. However rest shelter, drinking water huts & mobile toilets will be provided at site.

17.8 DISPOSAL OF MINING MACHINERIES

No big machineries will deploy in this work. The excavation of Brick Earth, transportation of kuchha bricks are by manual means. The other machineries, moulds etc not disposed during the period of the project.

17.9 SAFETY AND SECURITY

For safety purpose the following proposals are proposed:

As the project will be for 5 years thus it is proposed to fence the excavated area to check the excavated area to check the inadvertent entry of human and live stock after closed the mining operation.

The safe workings are proposed in the supervision of technical and qualified supervisory staff provided as per Mines Act. Safety measures will be the personal protective equipment will be provided to the labourers.

17.10. DISASTER MANAGEMENT PLAN AND RISK ASSESSMENT

No landslide in this area is observed.

The workings are proposed from top to bottom by forming proper benching. The proposed workings will be by opencast mining method. Underground mining is not proposed. Face height will maintain safe. No tailing dam is proposed. Thus high -risk accidents like land slide, subsidence, flood, inundation, fire, seismic activities etc. not come across. Dispensary is available near the area.

17.11CARE AND MAINTENANCE DURING TEMPORARY DISCONTINUANCE

Not applicable.

ONOMIC RESIDENTS MINE AND MANPOWER RETRENCHMENT

18.1 NUMBER OF LOCAL RESIDENTS EMPLOYED

Around 38 labourers will be engaged per day during the period of this project.

18.2 COMPENSATION

The compensation to the employees with sustenance of himself and their family members will be provided as per Labour Law and Mines Act.

18.3 SATELLITE OCCUPATIONS CONNECTED WITH MINING INDUSTRY

Some people will get satellite occupations during the period of project only.

18.4 CONTINUED ENGAGEMENT OF EMPLOYMENT IN THE REHABILITATED STATUS OF MINING LEASE AREA AND ANY OTHER REMNANT ACTIVITIES

Not applicable in this mine closure plan.

18.5 ENVISAGED REPERCUSSIONS ON THE EXPECTATION OF THE SOCIETY AROUND DUE TO CLOSURE OF MINE

Nil.

18.6 TIME SCHEDULING FOR ABANDONMENT

The project will be for 5 years. The working will close after the period for which EC is given. The excavated area will be fenced at the end of closing of working. The trees will be planted along the kuchha approach road, around the excavated area and along the tar road. Trees will be planted in each monsoon. Total 250 trees will be planted during the period of the project around the excavation site.

18.7 ABANDONED COST

Abandoned cost is within the financial assurance deposited by the project proponent.

19.0 BUDGETS FOR MINE CLOSURE

S. No.	Particulars	Amount (lakhs)
1	Maintaining bund wall & plantation on benches	0.1
2	Leveling and landscaping of flat pit area and making it fit for cultivation.	0.1
TOTAL		**0.2**

20.0 ANALYSIS OF PROPOSAL (FINAL RECOMMENDATION)

Overall the project will have positive and long term impact on environment. The project will also bring positive changes in terms of socio economic development by way of generating direct and indirect employment opportunities to the people vicinity. Also the project will bring economic benefit to the state in terms of revenue generation

****

LOCATION PLAN, KEY PLAN, AREA PLAN, (Annexure I)

Typical Plan & Section of Soil Mining

INDEX

PLATE NO. 1

LOCATION PLAN

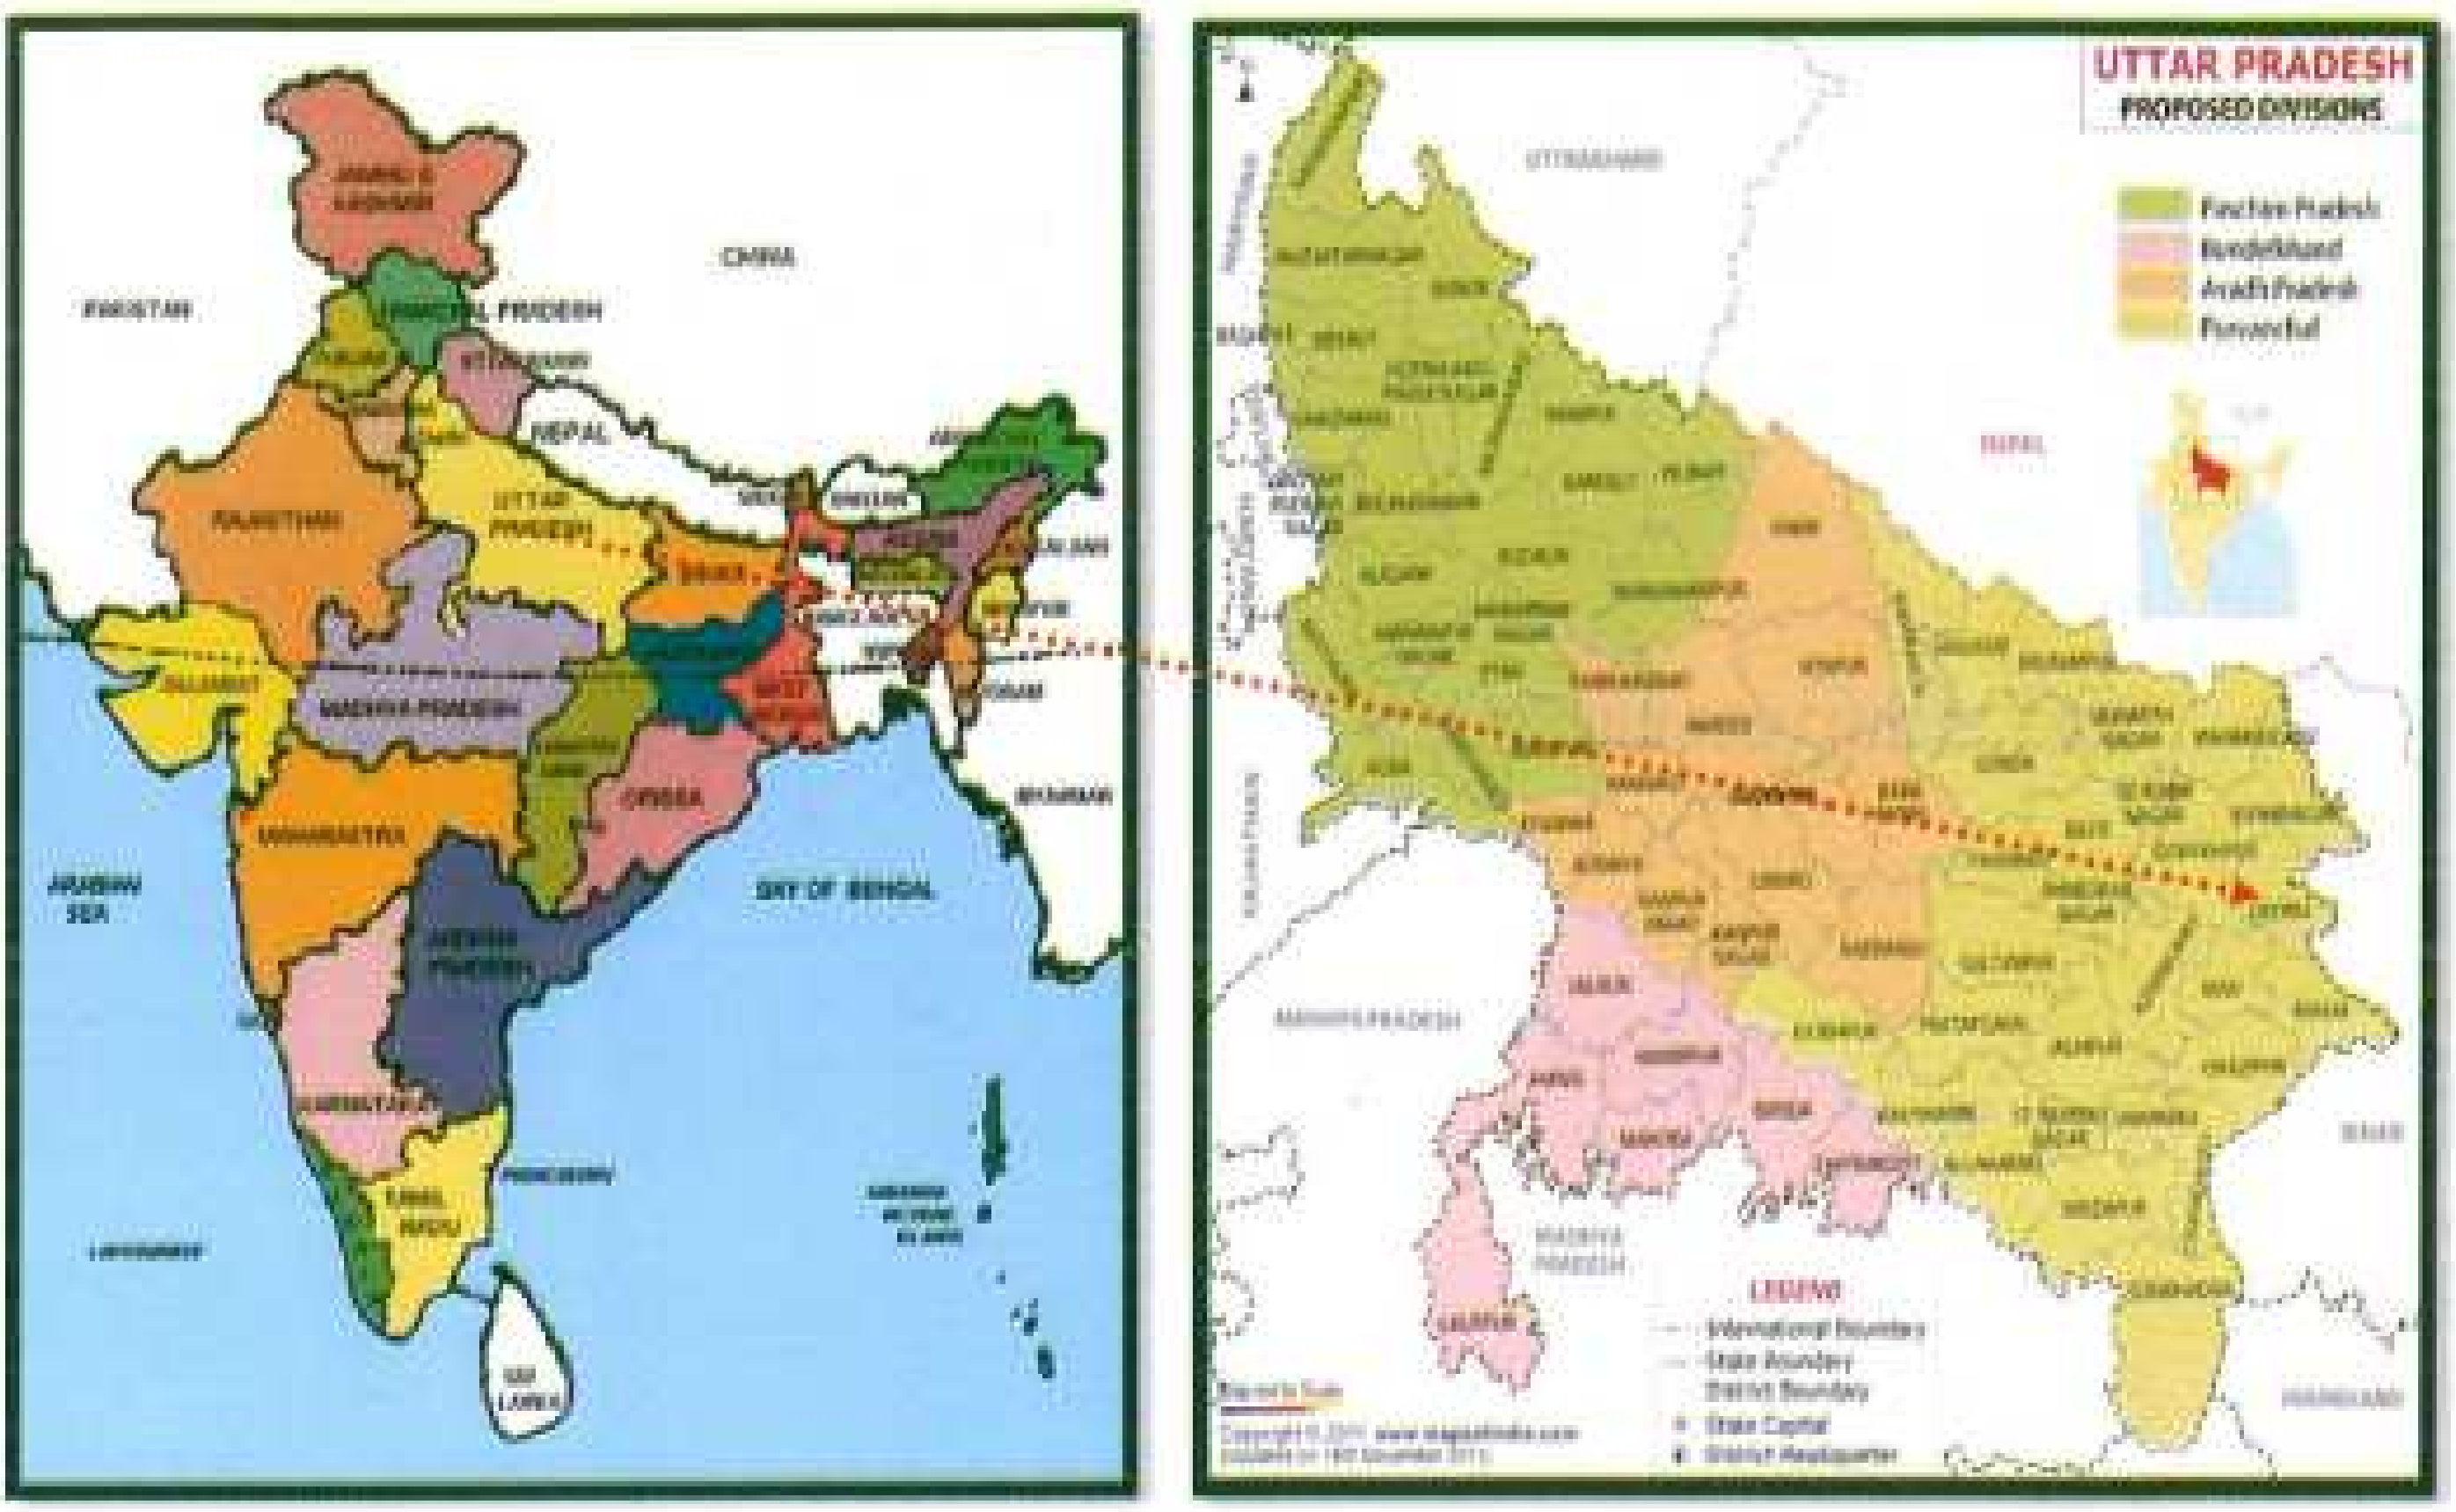

M/s UDAIPUR MIN TECH PVT. LTD.
RQP/UDP/354/2009/B

Typical Plan & Section of Soil Mining

PLAN-BUFFER ZONE GOOGLE IMAGE SHOWING 5 KM RADIUS AREA

PLATE No. 2

M/s UDAIPUR MIN TECH PVT. LTD.
RQP/UDR/354/2009/B

Typical Plan & Section of Earth Mining

Plate No. 3

TYPICAL PLAN & SECTIONS OF BRICK EARTH MINING

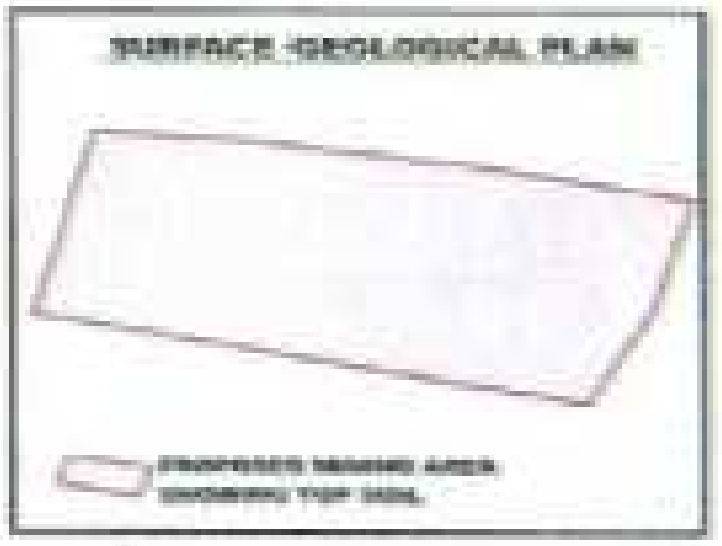

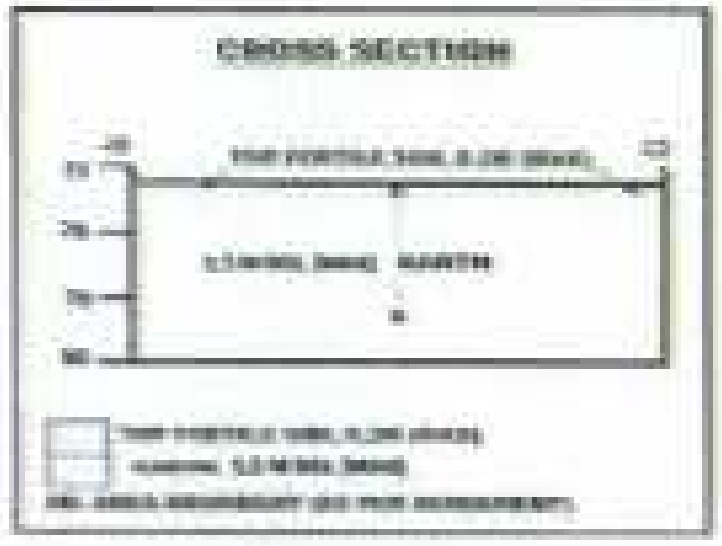

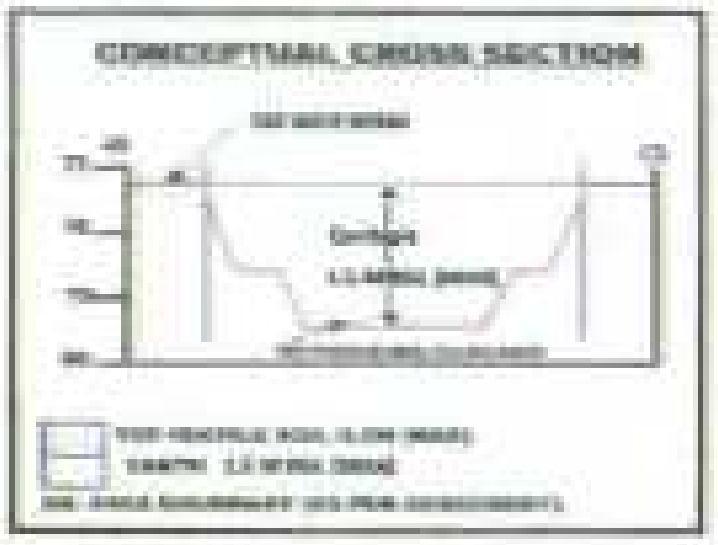

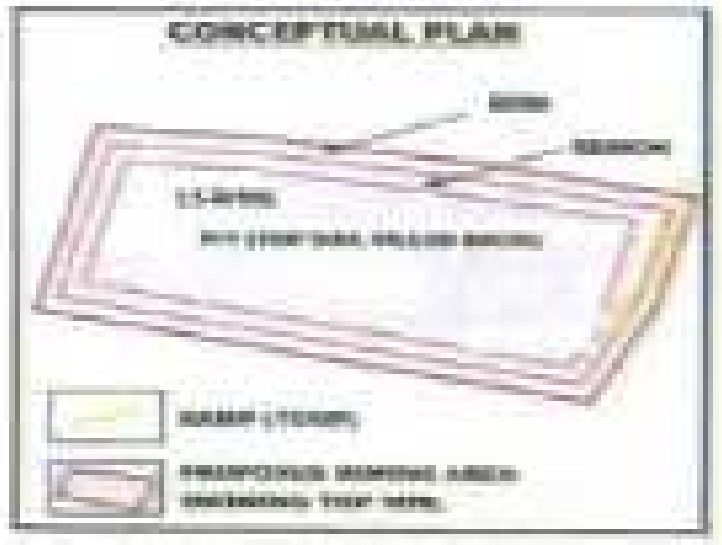

PLATE NO. 3

M/S UDAIPUR MIN-TECH PVT. LTD.
RQP/UDP/354/2009/B

AGREEMENT PAPER
(Annexure II)

भारतीय गैर न्यायिक

पचास रुपये

FIFTY RUPEES

Rs.50

NOTARIAL NOTARIAL

INDIA

INDIA NON JUDICIAL

उत्तर प्रदेश UTTAR PRADESH

AZ 915129

मिट्टी एग्रीमेंट

हम कि रामईश्वर यादव पुत्र शारदा यादव ग्राम–वालपुर, श्रीनगर, पो0–तरकुलवा, तहसील व जिला–देवरिया

प्रथम पक्ष
रामईश्वर

एवं

मैं शिवम ईंट उद्योग वालपुर श्रीनगर पो0–तरकुलवा, तहसील व जिला–देवरिया

द्वितीय पक्ष

प्रोपराइटर रामअशीष गुप्ता पुत्र स्व0 वंशी गुप्ता

प्रथम पक्ष आ0सं0 96 रकबा 0.279 हे0 लगानी 9 रुपये 10 पैसे, परगना शाहजहापुर, तहसील व जिला देवरिया के पूर्ण भाग के मालिक, काबिज व दाखिल है। हम प्रथम पक्ष उक्त आराजी हर प्रकार से पाक एवं साफ है। इसकी मिट्टी उठाने के पूर्ण हक प्राप्त है। व जरूरत खर्चा, खानगी हमने अपनी उपरोक्त आराजी के कुल भाग में से मिट्टी उठान का करार पत्र मुबलिक ……15,000/–रूपया प्रति बिगहा से 5 फुट गहराई तक 5 वर्ष के लिए द्वितीय पक्ष शिवम ईंट उद्योग वालपुर श्रीनगर पो0–तरकुलवा, तहसील व जिला–देवरिया उपरोक्त को दे दिया है। शर्त यह है कि–

भारतीय गैर न्यायिक

पचास रुपये

FIFTY RUPEES

रु.50

Rs.50

INDIA

INDIA NON JUDICIAL

उत्तर प्रदेश UTTAR PRADESH

AZ 915130

1. हम प्रथम पक्ष मिट्टी कटाने में कोई बाधा नही डालेगें, न हमारे परिवार का सदस्य बाधा उत्पन्न करेगा, यदि कोई बाधा उत्पन्न करेगा तो हम प्रथम पक्ष की पूर्ण जिम्मेदारी होगी।

2. मिट्टी कटान प्रथम पक्ष 5 फुट गहराई तक मान्य है।

3. मिट्टी की कीमत प्रथम पक्ष के द्वितीय पक्ष से — रुपया प्रति बिघा तय है।

4. हम प्रथम पक्ष को द्वितीय पक्ष ने — रुपया एडवान्स दिया है।

5. हम प्रथम पक्ष ने जो भी जमीन द्वितीय पक्ष को दि है उसे हम फर्म के द्वारा नाप के अनुसार ही रुपया लेगें। और शेष रुपया आगे तक दिया जायेगा।

6. यह कि हम प्रथम पक्ष का द्वितीय पक्ष से मिट्टी उठान का करार 10 जनवरी 2016 से 9 जनवरी 2021 तक तय किया गया है।

7. यह कि द्वितीय पक्ष की खेत समतल कराने की कोई जिम्मेदारी नही होगी।

211/11

उद्धरण खतौनी

ग्राम क्रमांक : 55010200449 ग्राम का नाम : खालपुर श्रीनगर परगना : शाहजहाँपुर तहसील : देवरिया
जनपद : देवरिया फसली वर्ष : 1420-1425 भाग : 1

खाता खतौनी का संख्या	खातेदार का नाम	पिता / पति / संरक्षक का नाम	निवास स्थान	भौमिक अधिकार प्रारम्भ होने का फसली वर्ष	खाते के प्रत्येक गाटे की खसरा संख्या	प्रत्येक गाटे का क्षेत्रफल (हे.)	खातेदार द्वारा देय मालगुजारी या लगान	परिवर्तन सम्बन्धी आज्ञा या उसका संदर्भ उसकी संख्या तथा दिनांक सहित और आज्ञा देने वाले अधिकारी का पद	टिप
1	2			3	4	5	6	7-12	
श्रेणी : 1-क	भूमि जो संक्रमणीय भूमिधरों के अधिकार में हो।								
00148	रामप्रवेश पत्नी	शारदा शारदा	नि. ग्राम नि. ग्राम	1383फ़०	96	0.279			
				कुल गाटे : 1	कुल क्षे :	0.279	9.10		

सत्य प्रतिलिपि प्रमाणित

हस्ताक्षर
तहसीलदार / नायब तहसीलदार

भारतीय गैर न्यायिक

पचास रुपये

FIFTY RUPEES

Rs.50

NOTARIAL NOTARIAL

INDIA

INDIA NON JUD

उत्तर प्रदेश UTTAR PRADESH

AZ 915125

Attested

मिट्टी एग्रीमेंट

हम कि रामअशीष पुत्र वंशी ग्राम–वालपुर श्रीनगर, पो0–तरकुलवा, तहसील व जिला–देवरिया

प्रथम पक्ष

एवं

मै शिवम ईंट उद्योग वालपुर श्रीनगर पो0–तरकुलवा, तहसील व जिला–देवरिया

द्वितीय पक्ष

प्रोपराइटर रामअशीष गुप्ता पुत्र स्व0 वंशी गुप्ता

प्रथम पक्ष आ0सं0 116 रकबा 0.174 हे0 लगानी 6 रुपये 85 पैसे, परगना शाहजहांपुर, तहसील व जिला देवरिया के पूर्ण भाग के मालिक, काबिज व दाखिल है। हम प्रथम पक्ष उक्त आराजी हर प्रकार से पाक एवं साफ है। इसकी मिट्टी उठाने के पूर्ण हक प्राप्त है। व जरूरत खर्चा, खानगी हमने अपनी उपरोक्त आराजी के कुल भाग में से मिट्टी उठान का करार पत्र मुगलिक ......16,000/-...... रुपया प्रति बिगहा से 5 फुट गहराई तक 5 वर्ष के लिए द्वितीय पक्ष शिवम ईंट उद्योग वालपुर श्रीनगर पो0–तरकुलवा तहसील व जिला–देवरिया उपरोक्त को दे दिया है। शर्त यह है कि–

भारतीय गैर न्यायिक

पचास रुपये

FIFTY RUPEES

रु.50

Rs.50

INDIA

INDIA NON JUDICIAL

उत्तर प्रदेश UTTAR PRADESH AZ 915126

1. हम प्रथम पक्ष मिट्टी कटाने में कोई बाधा नही डालेंगे, न हमारे परिवार का सदस्य बाधा उत्पन्न करेगा, यदि कोई बाधा उत्पन्न करेगा तो हम प्रथम पक्ष की पूर्ण जिम्मेदारी होगी।

2. मिट्टी कटान प्रथम पक्ष 5 फुट गहराई तक मान्य है।

3. मिट्टी की कीमत प्रथम पक्ष के द्वितीय पक्ष से —— रूपया प्रति बिघा तय है।

4. हम प्रथम पक्ष को द्वितीय पक्ष ने —— रूपया एडवान्स दिया है।

5. हम प्रथम पक्ष ने जो भी जमीन द्वितीय पक्ष को दि है उसे हम फर्म के द्वारा नाप के अनुसार ही रूपया लेगें। और शेष रूपया आगे तक दिया जायेगा।

6. यह कि हम प्रथम पक्ष का द्वितीय पक्ष से मिट्टी उठान का करार 10 जनवरी 2016 से 9 जनवरी 2021 तक तय किया गया है।

7. यह कि द्वितीय पक्ष की खेत समतल कराने की कोई जिम्मेदारी नही होगी।

183

उद्धरण खतौनी

ग्राम क्रमांक : 55010200449 ग्राम का नाम : बालपुर श्रीनगर परगना : शाहजहाँपुर तहसील : देवरिया

जनपद : देवरिया फसली वर्ष : 1420-1425 भाग : 1

खाता खतौनी क्रम संख्या	खातेदार का नाम	पिता / पति / संरक्षक का नाम	निवास स्थान	भौमिक अधिकार प्रारम्भ होने का फसली वर्ष	खाते के प्रत्येक गाटे की खसरा संख्या	प्रत्येक गाटे का क्षेत्रफल (हे.)	खातेदार द्वारा देय मालगुजारी या लगान	परिवर्तन सम्बन्धी आज्ञा या उसका संराश उनकी संख्या तथा दिनांक सहित और आज्ञा देने वाले अधिकारी का पद	टि
1	2			3	4	5	6	7-12	
श्रेणी : 1-क	भूमि जो संक्रमणीय भूमिधरों के अधिकार में हो।								
00054	[illegible]	सरल	नि. ग्राम	1383फ0	116	0.174			
	[illegible]	वही	नि. ग्राम	1383फ0	2368	0.093			
	[illegible]	वही	नि. ग्राम						
	[illegible]	वही	नि. ग्राम						
	[illegible]	वही	नि. ग्राम						
	[illegible]	वही	नि. ग्राम						
				कुल गाटे :	2	कुल क्षे : 0.267	6.85		

सत्य प्रतिलिपि [illegible]

हस्ताक्षर
लेखपाल / नायब तहसीलदार

1/11/2016

पृष्ठ संख्या



[illegible]

भारतीय गैर न्यायिक

पचास रुपये

FIFTY RUPEES

Rs.50

NOTARIAL NOTARIAL

INDIA

INDIA NON JUD

उत्तर प्रदेश UTTAR PRADESH

AZ 915128

मिट्टी एग्रीमेंट

हम कि रामप्रवेश यादव पुत्र श्री श्रवण यादव ग्राम–बालपुर श्रीनगर, पो0–तरकुलवा, तहसील व जिला–देवरिया

प्रथम पक्ष

एवं

मै शिवम ईंट उद्योग बालपुर श्रीनगर पो0–तरकुलवा, तहसील व जिला–देवरिया

द्वितीय पक्ष

प्रोपराइटर रामअशीष गुप्ता पुत्र स्व0 वंशी गुप्ता

प्रथम पक्ष आ0सं0 49 रकबा 0.210 हे0 लगानी 5 रुपये 20 पैसे परगना शाहजहापुर, तहसील व जिला देवरिया के पूर्ण भाग के मालिक, काबिज व दाखिल है। हम प्रथम पक्ष उक्त आराजी हर प्रकार से पाक एव साफ है। इसकी मिट्टी उठाने के पूर्ण हक प्राप्त है। व जरूरत खर्चा, खानगी हमने अपनी उपरोक्त आराजी के कुल भाग में से मिट्टी उठाने का करार पत्र मुगलिक .....18,000/-.... रुपया प्रति बिगहा से 5 फुट गहराई तक 5 वर्ष के लिए द्वितीय पक्ष शिवम ईंट उद्योग बालपुर श्रीनगर पो0–तरकुलवा, तहसील व जिला–देवरिया उपरोक्त को दे दिया है। शर्त यह है कि–

भारतीय गैर न्यायिक

पचास रुपये

FIFTY RUPEES

Rs.50

INDIA

NOTARIAL

NOTARIAL

INDIA NON JUDICIAL

उत्तर प्रदेश UTTAR PRADESH AZ 915127

1. हम प्रथम पक्ष मिट्टी कटाने में कोई बाधा नही डालेगें, न हमारे परिवार का सदस्य बाधा उत्पन्न करेगा, यदि कोई बाधा उत्पन्न करेगा तो हम प्रथम पक्ष की पूर्ण जिम्मेदारी होगी।

2. मिट्टी कटान प्रथम पक्ष 5 फुट गहराई तक मान्य है।

3. मिट्टी की कीमत प्रथम पक्ष के द्वितीय पक्ष से —— रूपया प्रति विघा तय है।

4. हम प्रथम पक्ष को द्वितीय पक्ष ने —— रूपया एडवान्स दिया है।

5. हम प्रथम पक्ष ने जो भी जमीन द्वितीय पक्ष को दि है उसे हम फर्म के द्वारा नाप के अनुसार ही रूपया लेगें। और शेष रूपया आगे तक दिया जायेगा।

6. यह कि हम प्रथम पक्ष का द्वितीय पक्ष से मिट्टी उठान का करार 10 जनवरी 2016 से 9 जनवरी 2021 तक तय किया गया है।

7. यह कि द्वितीय पक्ष की खेत समतल कराने की कोई जिम्मेदारी नही होगी।

910
11.1.

ग्राम कोड : 55610200435 ग्राम का नाम : जमुनी तप्पा परगना : शाहजहाँपुर तहसील : देवरिया
जनपद : देवरिया फसली वर्ष : 1418-1423 भाग : 1

खाता खतौनी क्रम संख्या	खातेदार का नाम	पिता / पति / संरक्षक का नाम	निवास स्थान	भौमिक अधिकार प्रारम्भ होने का फसली वर्ष	खाते के प्रत्येक गाटे की खसरा संख्या	प्रत्येक गाटे का क्षेत्रफल (हे.)	खातेदार द्वारा देय मालगुजारी या लगान	परिवर्तन सम्बन्धी आज्ञा या उसका संराश उनकी संख्या तथा दिनांक सहित और आज्ञा देने वाले अधिकारी का पद	टिप्प
1	2			3	4	5	6	7-12	1
श्रेणी : 1-क	भूमि जो संक्रमणीय भूमिधरों के अधिकार में हो।								
[illegible]	[illegible]	सरवन	नि. ग्राम बालपुर श्रीनगर	1388फ	49	0.210			
	[illegible]	सरवन	नि. ग्राम बालपुर श्रीनगर						
	[illegible]	सरवन	नि. ग्राम बालपुर श्रीनगर						
	[illegible]	सरवन	नि. ग्राम बालपुर श्रीनगर						
	[illegible]	सरवन	नि. ग्राम बालपुर श्रीनगर						
				कुल गाटे : 1	कुल क्षे :	0.210	5.20		

सत्य प्रतिलिपि प्रमाणित

910 हस्ताक्षर
लेखपाल / कार्यवाहक तहसीलदार

[illegible]

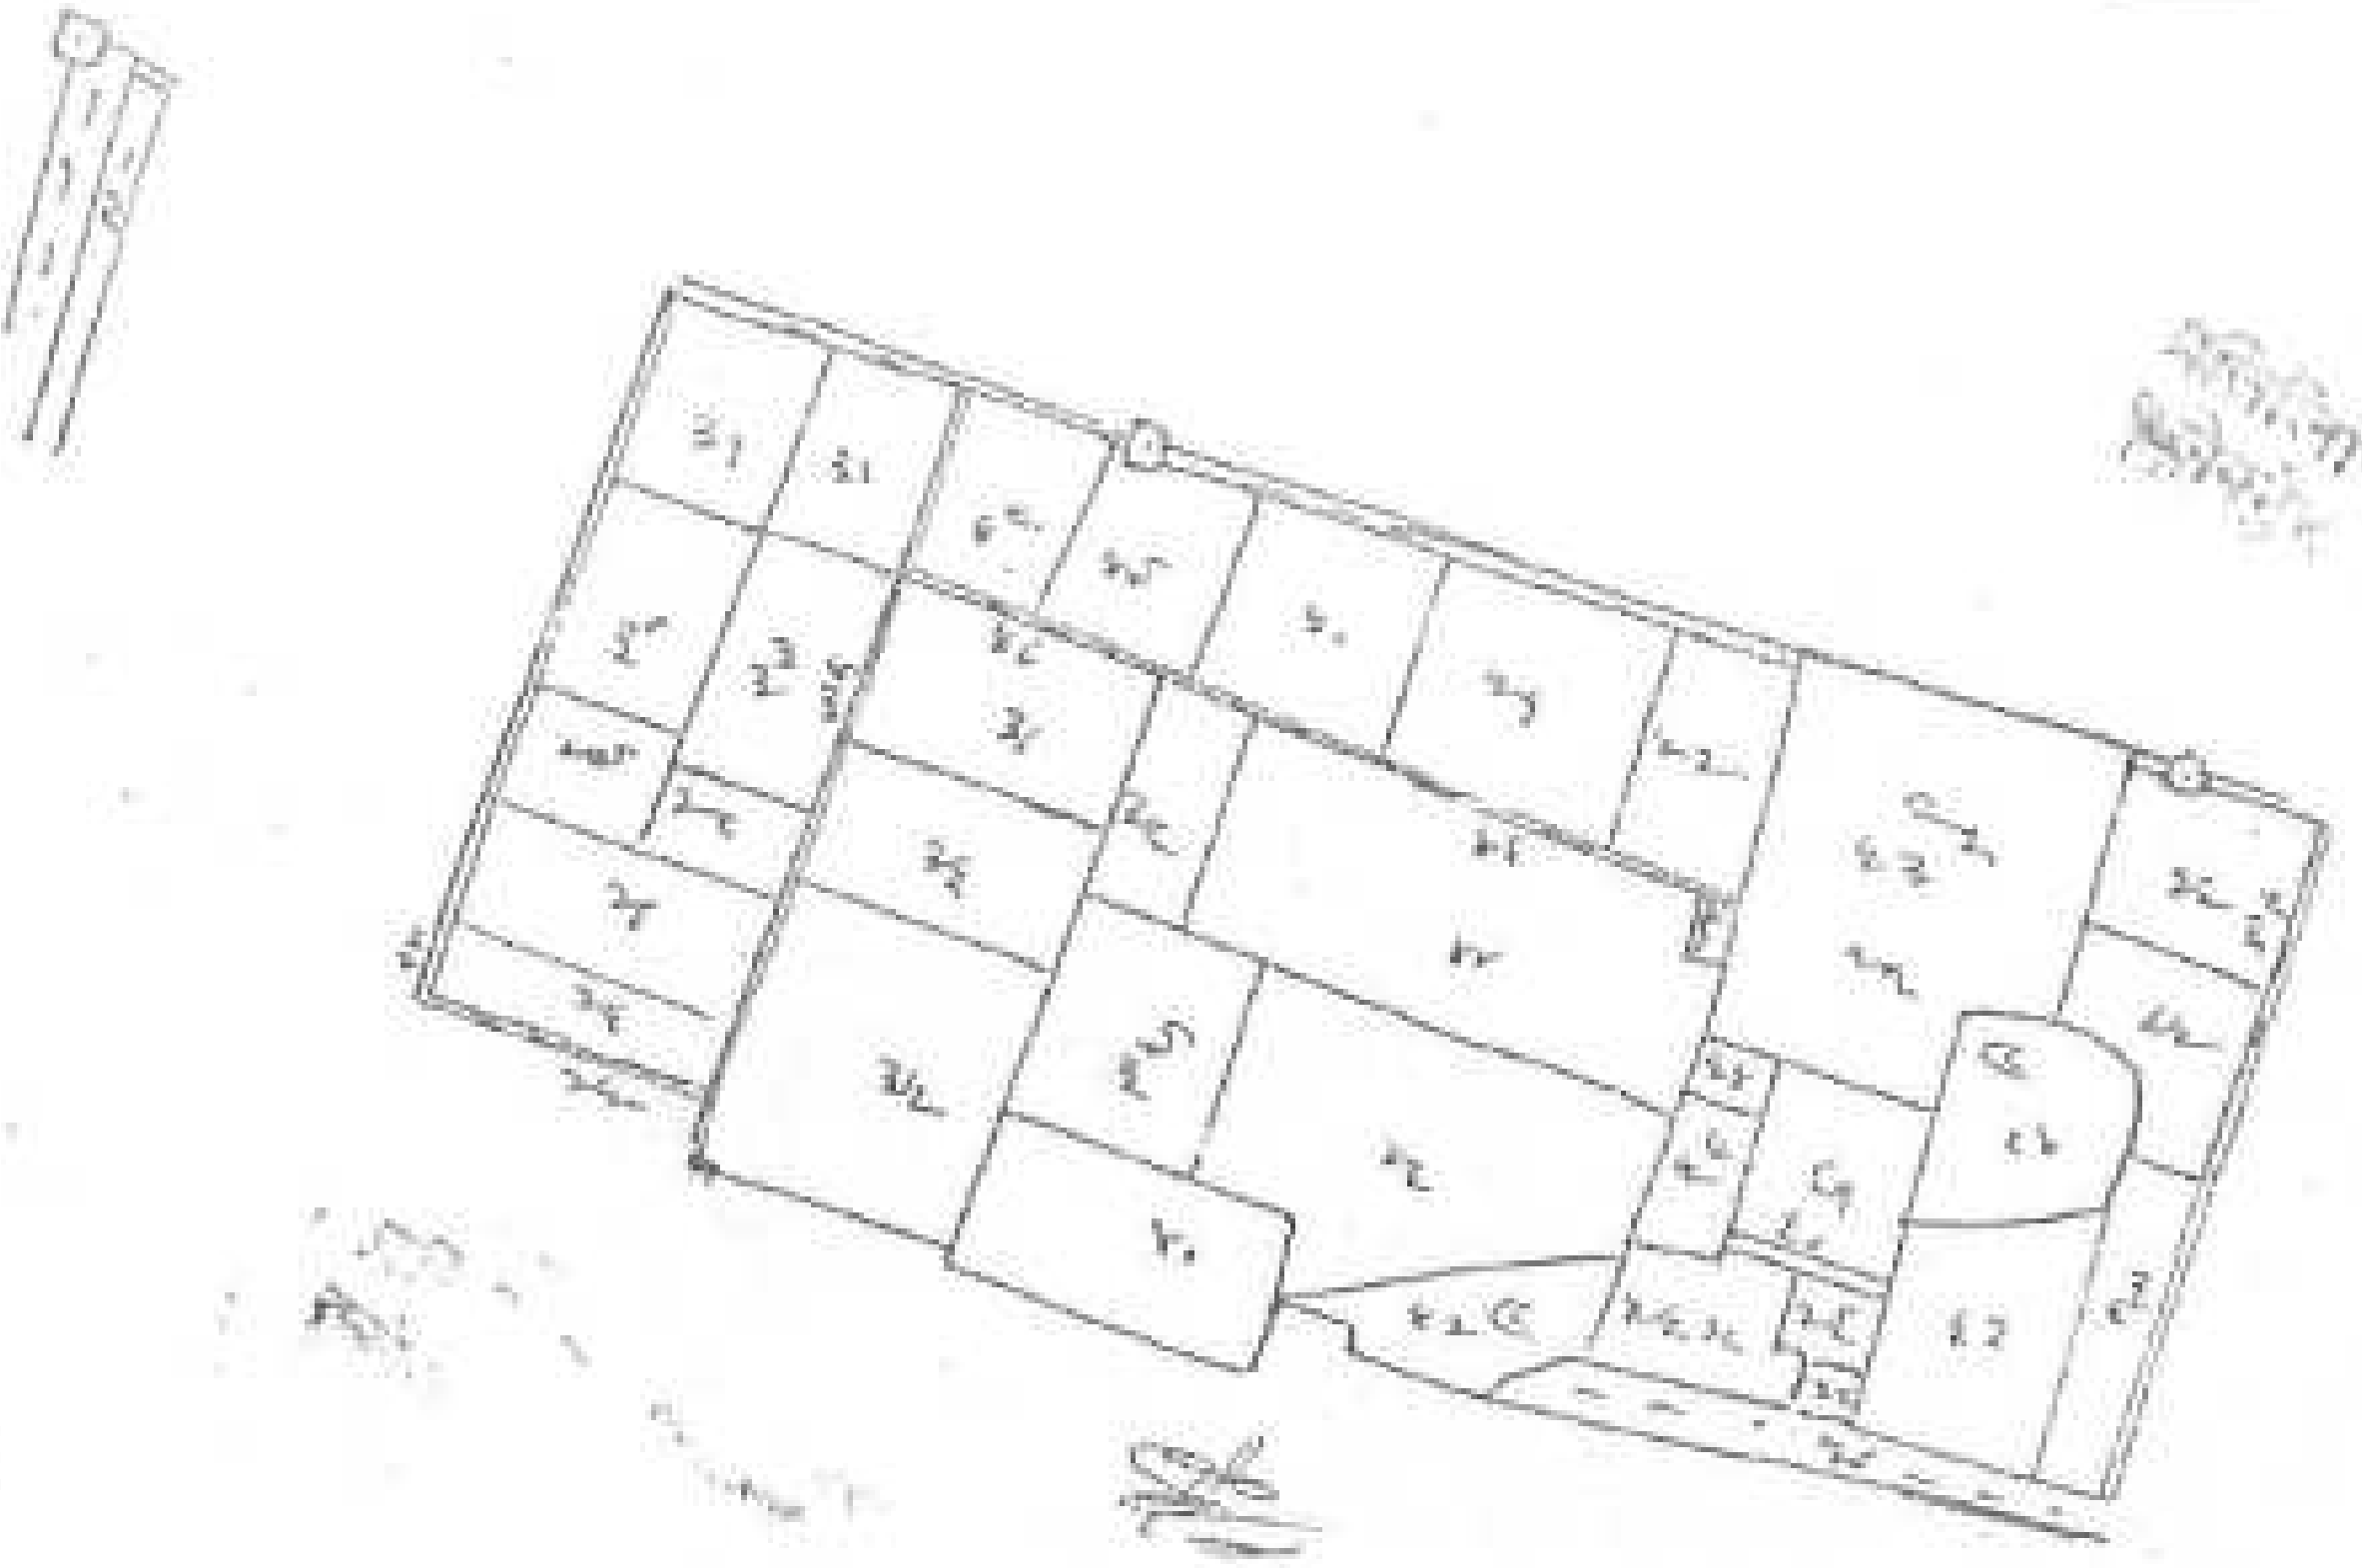

14-1-16

5909
13/1/16

भारतीय गैर न्यायिक

पचास रुपये

FIFTY RUPEES

NOTARIAL NOTARIAL

ATTESTED

Advocate Notary Deoria

INDIA

INDIA NON JUDICIAL

उत्तर प्रदेश UTTAR PRADESH

मिट्टी एग्रीमेन्ट

BF 011764

हम कि गोरख पुत्र कुलराज ग्राम लक्ष्मीपुर पो0 तरकुलवा तहसील व जिला देवरिया ।

प्रथम पक्ष

एवं

मै0 शिवम ईंट उद्योग बालपुर श्री नगर पो0 तरकुलवा तहसील व जिला देवरिया

द्वितीय पक्ष

प्रोपराइटर रामआशीष गुप्ता पुत्र स्व0 [illegible] गुप्ता

प्रथम पक्ष आ0स0 319 रकबा 0-5730 हे0 18 रूपये 60 पैसे परगना शाहजहाँपुर तहसील व जिला देवरिया के पूर्ण भाग के मालिक काबिज व दाखिल है। हम प्रथम पक्ष उक्त आराजी हर प्रकार से पाक एवं साफ है। हमको मिट्टी उठाने व मिट्टी बेचने के पूर्ण हक प्राप्त है। व [illegible], [illegible] हमने अपनी उपरोक्त आराजी के कुछ भाग में से मिट्टी उठाने का करार पत्र मुताबिक 10,000/- रूपया प्रति बिगहा से 5 फुट गहराई तक 5 वर्षों के लिए द्वितीय पक्ष शिवम ईंट उद्योग बालपुर श्री नगर पो0 तरकुलवा तहसील व जिला देवरिया उपरोक्त को दे दिया है। शर्त यह है कि -

30-3-18

भारतीय गैर न्यायिक

पचास रुपये

FIFTY RUPEES

रू.50

Rs.50

INDIA

INDIA NON JUDICIAL

उत्तर प्रदेश UTTAR PRADESH 2 BF 011765

1- हम प्रथम पक्ष मिट्टी काटने व उठाने मे कोई बाधा नही डालेगे, न हमारे परिवार का सदस्य बाधा उत्पन्न करेगा, यदि कोई बाधा उत्पन्न करेगा तो हम प्रथम पक्ष की पूर्ण जिम्मेदारी होगी ।

2- मिट्टी काटना प्रथम पक्ष 5 फुट गहराई तक मान्य है ।

3- मिट्टी की कीमत प्रथम पक्ष के द्वितीय पक्ष से —— रूपया प्रति बिघा तय है ।

4- हम प्रथम पक्ष को द्वितीय पक्ष ने —— रूपया एडवान्स दिया है ।

5- हम प्रथम पक्ष मे जो भी जमीन द्वितीय पक्ष को दि है उसे हम फार्म के द्वारा नाप के अनुसार ही रूपया लेगे ।और शेष रूपया आगे तक दिया जायेगा ।

6- यह कि हम प्रथम पक्ष का द्वितीय पक्ष से मिट्टी उठान का करार 1 जनवरी 2011 से 1 जनवरी 2023 तक तय किया गया है ।

7- यह कि द्वितीय पक्ष की खेत समतल करने की कोई जिम्मेदारी नहीं होगी ।

Suresh ... Srivastava

20-2-18

603 20-2-18

20-2-18

BHULEKH
Uttar Pradesh

निम्न खाते की प्रमाणित प्रति आनलाइन प्राप्त करने हेतु यहाँ क्लिक करें।

खाता विवरण (अप्रमाणित प्रति)

ग्राम का नाम : [illegible] उर्फ [illegible]   परगना : ([illegible])   तहसील : देवरिया   जनपद : देवरिया   फसली वर्ष : 1420-1425   भाग : 1   खाता संख्या : 00016

खातेदार का नाम / पिता पति संरक्षक का नाम / निवास स्थान	खसरा संख्या	क्षेत्रफल (हे.)	आदेश	टिप्पणी
श्रेणी : 1-क / भूमि जो संक्रमणीय भूमिधरों के अधिकार में हो				
[illegible] / [illegible] / नि. ग्राम	319	0.6760		
योग	1	0.6760		

Disclaimer: उक्त अभिलेख मात्र अवलोकनार्थ है, तहसील कम्प्यूटर केन्द्र एवम सी.एस.सी/लोकवाणी केन्द्र से उद्धरण की प्रमाणित प्रति प्राप्त की जा सकती है।

Software Powered By: National Informatics Center, Uttar Pradesh State Unit, Lucknow.

[illegible]

[illegible]

भारत

पचास रुपये

FIFTY RUPEES

Rs.50

NOTARIAL NOTARIAL

INDIA

NDIA NON JUD

उत्तर प्रदेश UTTAR PRADESH

AZ 915131

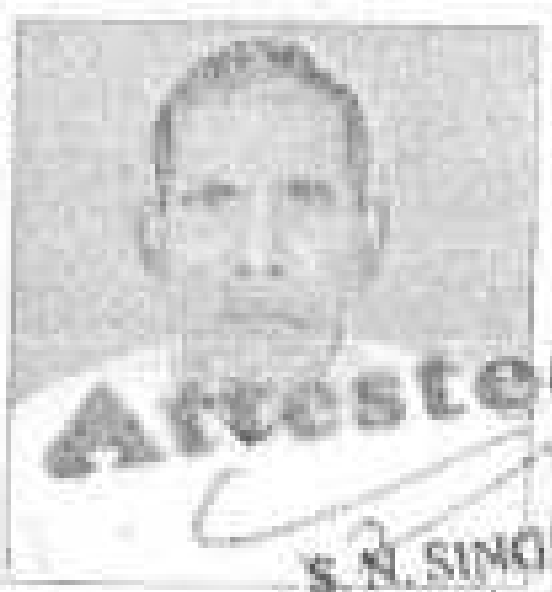

Attested

S. N. SING

Notary Collectorate

Distt. Deoria

मिट्टी एग्रीमेंट

हम कि काशी शर्मा पुत्र वंशी शर्मा ग्राम–बालपुर श्रीनगर, पो0–तरकुलवा, तहसील व जिला–देवरिया

प्रथम पक्ष

Kashisham

एवं

मै शिवम ईंट उद्योग बालपुर श्रीनगर पो0–तरकुलवा, तहसील व जिला–देवरिया

द्वितीय पक्ष

RamAshish

प्रोपराइटर रामअशीष गुप्ता पुत्र स्व0 वंशी गुप्ता

प्रथम पक्ष आ0सं0 148 रकबा 0.174 हे0 लगानी 22 रुपये 85 पैसे, परगना शाहजहापुर, तहसील व जिला देवरिया के पूर्ण भाग के मालिक, काबिज व दाखिल है। हम प्रथम पक्ष उक्त आराजी हर प्रकार से पाक एवं साफ है। इसकी मिट्टी उठाने के पूर्ण हक प्राप्त है। व जरूरत खर्चा, खानगी हमने अपनी उपरोक्त आराजी के कुल भाग में से मिट्टी उठान का करार पत्र मुगलिक ...15,000/- रूपया प्रति बिगहा से 5 फुट गहराई तक 5 वर्ष के लिए द्वितीय पक्ष शिवम ईंट उद्योग बालपुर श्रीनगर पो0–तरकुलवा, तहसील व जिला–देवरिया उपरोक्त को दे दिया है। शर्त यह है कि–

भारतीय गैर न्यायिक

पचास रुपये

FIFTY RUPEES

रु.50

Rs.50

INDIA

INDIA NON JUDICIAL

उत्तर प्रदेश UTTAR PRADESH

AZ 915132

1. हम प्रथम पक्ष मिट्टी कटाने में कोई बाधा नही डालेगें, न हमारे परिवार का सदस्य बाधा उत्पन्न करेगा, यदि कोई बाधा उत्पन्न करेगा तो हम प्रथम पक्ष की पूर्ण जिम्मेदारी होगी।

2. मिट्टी कटान प्रथम पक्ष 5 फुट गहराई तक मान्य है।

3. मिट्टी की कीमत प्रथम पक्ष के द्वितीय पक्ष से —— रूपया प्रति बिघा तय है।

4. हम प्रथम पक्ष को द्वितीय पक्ष ने —— रूपया एडवान्स दिया है।

5. हम प्रथम पक्ष ने जो भी जमीन द्वितीय पक्ष को दि है उसे हम फर्म के द्वारा नाप के अनुसार ही रूपया लेगें। और शेष रूपया आगे तक दिया जायेगा।

6. यह कि हम प्रथम पक्ष का द्वितीय पक्ष से मिट्टी उठान का करार 10 जनवरी 2016 से 9 जनवरी 2021 तक तय किया गया है।

7. यह कि द्वितीय पक्ष की खेत समतल कराने की कोई जिम्मेदारी नही होगी।

184
11-1-16

: 5507020049 ग्राम का नाम : बालपुर श्रीनगर परगना : शाहजहांपुर तहसील : देवरिया
: देवरिया फसली वर्ष : 1420-1425 भाग : 1

खातेदार का नाम	पिता / पति / संरक्षक का नाम	निवास स्थान	भौमिक अधिकार प्रारम्भ होने का फसली वर्ष	खाते के प्रत्येक गाटे की खसरा संख्या	प्रत्येक गाटे का क्षेत्रफल (हे.)	खातेदार द्वारा देय मालगुजारी या लगान	परिवर्तन सम्बन्धी आज्ञा या उसका सारांश उनकी संख्या तथा दिनांक सहित और आज्ञा देने वाले अधिकारी का पद	टिप्पणी
2			3	4	5	6	7-12	13
क भूमि जो संक्रमणीय भूमिधरी केअधिकार में हो।								
काशी	बंशी	नि. ग्राम	1383फ0	148	0.174			
			1383फ0	199अ	0.020			
			1383फ0	258	0.680			
			कुल गाटे :	3 कुल क्षे :	0.874	22.85		

सत्य प्रतिलिपि प्रमाणित

([illegible])
[illegible] नायब तहसीलदार
तह0-देवरिया सदर

Pollution NOC & Consent

(Annexure III)

Government of India

Form GST REG-06

[See Rule 10(1)]

Registration Certificate

Registration Number :09AIFPG5411N1Z5

1.	**Legal Name**	RAM ASHISH GUPTA			
2.	**Trade Name, if any**	M/S SHIVAM INT UDYOG			
3.	**Constitution of Business**	Proprietorship			
4.	**Address of Principal Place of Business**	1, BALPUR SRINAGAR, TARKULWA, Deoria, Uttar Pradesh, 274001			
5.	**Date of Liability**	01/07/2017			
6.	**Period of Validity**	From	01/07/2017	To	NA
7.	**Type of Registration**	Regular			
8.	**Particulars of Approving Authority**				

Signature

Name	
Designation	
Jurisdictional Office	
9. Date of issue of Certificate	26/10/2017

Note: The registration certificate is required to be prominently displayed at all places of business in the State.

This is a system generated digitally signed Registration Certificate issued based on the deemed approval of the application for registration

Annexure B

सत्यमेव जयते

GSTIN	09AIFPG5411N1Z5
Legal Name	RAM ASHISH GUPTA
Trade Name, if any	M/S SHIVAM INT UDYOG

Details of Proprietor

1 

Name	RAM ASHISH GUPTA
Designation/Status	PROPRITOER
Resident of State	Uttar Pradesh

वित्तीय नियम संग्रह खण्ड–5, भाग–2 कोषागार प्रपत्र–209 (1)

प्रपत्र संख्या–43 ए (1)

(प्रस्तार 417 एवं 478 देखिए)

धनराशि जमा करने का चालान फार्म

उपकोषागार/बैंक का नाम व शाखा भारतीय स्टेट बैंक देवरिया

1. जिस व्यक्ति (पदनाम यदि आवश्यक हो) या संस्था के नाम से धनराशि जमा की जा रही है उसका नाम प्रतीक मालवा [illegible] इण्टर कालेज

2. पता [illegible] इ० कालेज बालपुर [illegible] जिला - देवरिया

3. पंजीकरण संख्या/पक्ष का नाम व वाद संख्या (यदि आवश्यक हो) इं०-[illegible] शासकीय फीस वर्ष 2014-2015 (ग्यारह पाठे)

4. जमा की जा रही धनराशि का पूर्ण विवरण (धनराशि किस हेतु जमा की जा रही है तथा किस विभाग के पक्ष में जमा की जा रही है।) उनचालीस हजार एक सौ पचास मात्र 39,150.00

5. चालान की सकल राशि

6. चालान की निबल राशि

7. लेखाशीर्षक का पूर्ण विवरण/लेखाशीर्षक की मुहर :

8. लेखा शीर्षक का 13 डिजिट कोड

मुख्य लेखा शीर्षक	उप मुख्य शीर्षक	लघु शीर्षक	उप शीर्षक	ब्यौरावार शीर्षक	धनराशि (अंको में)
0853	00	102	00	01	39,150.00
					योग 39,150.00

धनराशि [illegible] उनचालीस हजार एक सौ पचास मात्र

[illegible] की पुष्टि करने वाले [illegible] के हस्ताक्षर मुहर सहित

जमाकर्ता का नाम व हस्ताक्षर प्रतीक मालवा

केवल उपकोषागार/बैंक के प्रयोगार्थ

रजिस्टर संख्या 101

दिनांक 15-12-2014

अंकों में रु०

शब्दों में रु०

भारतीय स्टेट बैंक देवरिया 19 DEC 2014 39150 सरकारी जमा

प्राप्त किया

प्राप्तकर्ता के हस्ताक्षर उपकोषागार/बैंक की मुहर सहित

वित्तीय नियम संग्रह खण्ड-5, भाग-2   कोषागार प्रपत्र-209 (1)
प्रपत्र संख्या 43 ए (1)
(प्रस्तर 417 एवं 478 देखिए)

धनराशि जमा करने का चालान-फार्म

उपकोषागार/बैंक का नाम व शाखा [illegible]

1. जिस व्यक्ति (पदनाम यदि आवश्यक हो) या संस्था के नाम से धनराशि जमा की जा रही है उसका नाम [illegible]
2. पता [illegible]
   जिला देवरिया
3. पंजीकरण संख्या/पक्ष का नाम व वाद संख्या (यदि आवश्यक हो) [illegible] आवेदन शुल्क
4. जमा की जा रही धनराशि का पूर्ण विवरण (धनराशि किस हेतु जमा की जा रही है तथा किस विभाग के पक्ष में जमा की जा रही है।) वर्ष 2014-2015 [illegible]
5. चालान की सकल राशि 2,000.00
6. चालान की निबल राशि
7. लेखाशीर्षक का पूर्ण विवरण/लेखाशीर्षक की मुहर :
8. लेखा शीर्षक का 13 डिजिट कोड

मुख्य लेखा शीर्षक	उप मुख्य शीर्षक	लघु शीर्षक	उप शीर्षक	ब्यौरेवार शीर्षक	धनराशि (अंको में)
0 4 5 3	0 0	1 0 2	0 5	0 1	2000.00
					/
				योग	2000.00

धनराशि (शब्दों में) दो हजार [illegible]

धनराशि/लेखाशीर्षक की पुष्टि करने वाले विभागीय अधिकारी के हस्ताक्षर मुहर सहित

जमाकर्ता का नाम व हस्ताक्षर

केवल उपकोषागार/बैंक के प्रयोगार्थ

चालान संख्या

दिनांक

अंकों में रु0

शब्दों में रु0

स्टेट बैंक
15 DEC 2014

प्राप्त किया
प्राप्तकर्ता के हस्ताक्षर उपकोषागार/
बैंक की मुहर सहित

वित्तीय नियम संग्रह खण्ड–5, भाग–2

प्रपत्र संख्या –43 ए (1)

(प्रस्तर 417 एवं 478 देखिए)

धनराशि जमा करने का चालान फार्म

कोषागार प्रपत्र – 209 (1)

C/10598769

उपकोषागार/बैंक का नाम व शाखा: ए-[illegible] हे [illegible]

1. जिस व्यक्ति (पदनाम यदि आवश्यक हो) या संस्था के नाम से धनराशि जमा की जा रही है उसका नाम: श्री रामप्रसाद [illegible]

2. पता: गांव देवरिया

3. पंजीकरण संख्या/पक्ष का नाम व वाद संख्या (यदि आवश्यक हो): भाटी

4. जमा की जा रही धनराशि का पूर्ण विवरण (धनराशि किस हेतु जमा की जा रही है तथा किस विभाग के पक्ष में जमा की जा रही है): जिला उद्योग [illegible] 39150-00
भारतीय उद्योग [illegible] 39150-00

5. चालान की सकल राशि: 78300-00

6. चालान की निबल राशि

7. लेखाशीर्षक का पूर्ण विवरण/लेखाशीर्षक की मुहर: 17/07/15 [illegible] 30-5-15 [illegible]
[illegible] 30/3/14

8. लेखा शीर्षक का 13 डिजिट कोड

मुख्य लेखा शीर्षक	उप मुख्य शीर्षक	लघु शीर्षक	उप शीर्षक	ब्यौरेवार शीर्षक	धनराशि (अंकों में)
0 8 5 2	0 0	1 0 2	0 0	0 1	
					39150-00
					39150-00
				योग	78300-00

धनराशि (शब्दों में) ~~[illegible]~~ अठहत्तर हजार तीन सौ मात्र

चालान में लेखा शीर्षक की पुष्टि करने वाले विभागीय अधिकारी के हस्ताक्षर मुहर सहित

श्री रामप्रसाद
जमाकर्ता का नाम व हस्ताक्षर

केवल उपकोषागार/बैंक के प्रयोगार्थ

चालान संख्या 32

दिनांक 31-7-15

अंकों में रू0 78300

शब्दों में रू0

प्राप्त किया

प्राप्तकर्ता के हस्ताक्षर उपकोषागार/
बैंक की मुहर सहित

31 JUL 2015

कोषागार प्रपत्र – 209 (1)

वित्तीय नियम संग्रह खण्ड–5, भाग–2

प्रपत्र संख्या –43 ए (1)

(प्रस्तर 417 एवं 478 देखिए)

धनराशि जमा करने का चालान फार्म

उपकोषागार/बैंक का नाम व शाखा

1. जिस व्यक्ति (पदनाम यदि आवश्यक हो) या संस्था के नाम से धनराशि जमा की जा रही है उसका नाम: इन्टेग्रो मेडिसीन
[illegible] नं० [illegible]

2. पता: [illegible] देवलिया
[illegible] वर्ष - 2013-2014
आवेदन शुल्क

3. पंजीकरण संख्या/पक्ष का नाम व वाद संख्या (यदि आवश्यक हो)

4. जमा की जा रही धनराशि का पूर्ण विवरण (धनराशि किस हेतु जमा की जा रही है तथा किस विभाग के पक्ष में जमा की जा रही है): रिन्यूअल (ड्रग) लाइसेंस 2000/-
और [illegible] 2000/-
योग [illegible]

5. चालान की सकल राशि

6. चालान की निबल राशि

7. लेखाशीर्षक का पूर्ण विवरण/लेखाशीर्षक की मुहर: ड्रग्स [illegible]
वर्ष 2013-2014

8. लेखा शीर्षक का 13 डिजिट कोड

मुख्य लेखा शीर्षक	उप मुख्य शीर्षक	लघु शीर्षक	उप शीर्षक	ब्यौरेवार शीर्षक	धनराशि (अंकों में)
0853	00	102	00	51	
					2000-00
					2000-00

धनराशि (शब्दों में) [illegible] हजार रु० मात्र .... योग [illegible]

चालान में लेखा शीर्षक की पुष्टि करने वाले विभागीय अधिकारी के हस्ताक्षर मुहर सहित

[illegible]
जमाकर्ता का नाम व हस्ताक्षर

केवल उपकोषागार/बैंक के प्रयोगार्थ

चालान संख्या

दिनांक

अंकों में रु०	
शब्दों में रु०	

31 DEC 2013

सरकारी [illegible]

प्राप्त किया

प्राप्तकर्ता के हस्ताक्षर उपकोषागार/बैंक की मुहर सहित

वित्तीय नियम संग्रह खण्ड-5, भाग- 2 कोषागार प्रपत्र-209 (1)
प्रपत्र संख्या-43 ए (1)
(प्रस्तर 417 एवं 478 देखिए)

धनराशि जमा करने का चालान फार्म

इकाई देवरिया

उपकोषागार/बैंक का नाम व शाखा मै० शिवम [illegible] उद्योग

1. जिस व्यक्ति (पदनाम यदि आवश्यक हो) या संस्था के नाम से धनराशि जमा की जा रही है उसका नाम द्वारा मनोज गुप्ता पुत्र वंशी गुप्ता ग्राम बल्लभपुर श्रीनगर तह० देवरिया वर्ष 2017-18 पाया 17
2. पता
3. पंजीकरण संख्या/पक्ष का नाम व वाद संख्या (यदि आवश्यक हो)
4. जमा की जा रही धनराशि का पूर्ण विवरण (धनराशि किस हेतु जमा की जा रही है तथा किस विभाग के पक्ष में जमा की जा रही है।) आवेदन शुल्क
5. चालान की सकल राशि
6. चालान की निबल राशि
7. लेखाशीर्षक का पूर्ण विवरण/लेखाशीर्षक की मुहर :
   0853 अलौह खनन [illegible]
   102 खनिज रि[illegible]
   स्वत्व शुल्क 01 [illegible]
   किराया एवं स्वत्व शुल्क।
8. लेखा शीर्षक का 13 डिजिट कोड

मुख्य लेखा शीर्षक	उप मुख्य शीर्षक	लघु शीर्षक	उप शीर्षक	ब्यौरावार शीर्षक	धनराशि (अंको मे)
0853	00	102	00	01	2000/-

धनराशि (शब्दो में) रू० दो हजार रू० मात्र .... योग 2000/-

चालान में लेखा शीर्षक की पुष्टि करने वाले विभागीय अधिकारी के हस्ताक्षर मुहर सहित

-11-17

श्रीराम यादव
जमाकर्ता का नाम व हस्ताक्षर

केवल उपकोषागार/बैंक के प्रयोगार्थ

चालान संख्या

दिनांक.........

अंकों में रु0

शब्दों में रु0

प्राप्त किया
प्राप्तकर्ता के हस्ताक्षर उपकोषागार/बैंक की मुहर सहित

वित्तीय नियम संग्रह खण्ड-5, भाग- 2 कोषागार प्रपत्र-209 (1)
प्रपत्र संख्या-43 ए (1)
(प्रस्तर 417 एवं 478 देखिए)

धनराशि जमा करने का चालान फार्म

ड्रा.उ.र देवरिया

उपकोषागार/बैंक का नाम व शाखा — मे. शिवम टेन्ट उद्योग

1. जिस व्यक्ति (पदनाम यदि आवश्यक हो) या संस्था के नाम से धनराशि जमा की जा रही है उसका नाम — प्रो. राम प्रदीप गुप्ता पुत्र वंशी गुप्ता ग्रा० कतरपुर कोनगर तह. देवरिया वर्ष 2017-18 पाया 17
2. पता
3. पंजीकरण संख्या/पक्ष का नाम व वाद संख्या (यदि आवश्यक हो)
4. जमा की जा रही धनराशि का पूर्ण विवरण (धनराशि किस हेतु जमा की जा रही है तथा किस विभाग के पक्ष में जमा की जा रही है।) — आवेदन शुल्क
5. चालान की सकल राशि
6. चालान की निवल राशि
7. लेखाशीर्षक का पूर्ण विवरण/लेखाशीर्षक की मुहर : — 0853 अलौह खनन एवं धातु कर्म उद्योग 102 खनिज रियायत शुल्क किराया एवं स्वत्व शुल्क 01 खनिज रियायत शुल्क किराया एवं स्वत्व शुल्क।
8. लेखा शीर्षक का 13 डिजिट कोड

मुख्य लेखा शीर्षक	उप मुख्य शीर्षक	लघु शीर्षक	उप शीर्षक	ब्यौरावार शीर्षक	धनराशि (अंको में)
0853	00	102	00	01	2000/-
					/

धनराशि (शब्दो में)......रु० दो हजार केवल...... योग 2000/-

चालान में लेखा शीर्षक की पुष्टि करने वाले विभागीय अधिकारी के हस्ताक्षर मुहर सहित

लेखा लिपिक
10-11-17

प्रेमराम यादव
आवेदक, व्यक्ति/जमाकर्ता का नाम व हस्ताक्षर

केवल उपकोषागार/बैंक के प्रयोगार्थ

चालान संख्या

दिनांक.......

अंकों में रु0

शब्दों में रु0

प्राप्त किया

प्राप्तकर्ता के हस्ताक्षर उपकोषागार/बैंक की मुहर सहित

भारतीय स्टेट बैंक
शाखा - देवरिया
10 NOV 17

वित्तीय नियम संग्रह खण्ड-5, भाग- 2 कोषागार प्रपत्र-209 (1)
प्रपत्र संख्या-43 ए (1)
(प्रस्तर 417 एवं 478 देखिए)

धनराशि जमा करने का चालान फार्म

0917031256

उपकोषागार/बैंक का नाम व शाखा S.B.I देवरिया [illegible]

1. जिस व्यक्ति (पदनाम यदि आवश्यक हो) या संस्था के नाम से धनराशि जमा की जा रही है उसका नाम प्रो० राम अशीष गुप्ता S/o वंशी गुप्ता

2. पता ग्रा० बालपुर सोनगार तह० देवरिया, जि० देवरिया
वर्ष 2017-18 फार्म 17

3. पंजीकरण संख्या/पक्ष का नाम व वाद संख्या (यदि आवश्यक हो) ईंट पथाई हेतु मिट्टी रॉयल्टी

4. जमा की जा रही धनराशि का पूर्ण विवरण (धनराशि किस हेतु जमा की जा रही है तथा किस विभाग के पक्ष में जमा की जा रही है।)

5. चालान की सकल राशि

6. चालान की निबल राशि

7. लेखाशीर्षक का पूर्ण विवरण/लेखाशीर्षक की मुहर : 0853-अलौह धातु तथा धातु कर्म उद्योग
800-खनिज रियायती शुल्क किराया और स्वत्व
खनिज रियायत शुल्क किराया और स्वत्व

8. लेखा शीर्षक का 13 डिजिट कोड

मुख्य लेखा शीर्षक	उप मुख्य शीर्षक	लघु शीर्षक	उप शीर्षक	ब्यौरावार शीर्षक	धनराशि (अंको में)
0853	00	800	00	01	86130/=

धनराशि (शब्दो में)...रु० छियासी हजार एक सौ तीस रु० मा० योग 86130/=

चालान में लेखा शीर्षक की पुष्टि करने वाले विभागीय अधिकारी के हस्ताक्षर मुहर सहित

रामअशीष
जमाकर्ता का नाम व हस्ताक्षर

केवल उपकोषागार/बैंक के प्रयोगार्थ

चालान संख्या 57

दिनांक...............

10 NOV 2017

86130

अंकों में रु0

शब्दों में रु0

प्राप्त किया
प्रापकर्ता के हस्ताक्षर उपकोषागार/
बैंक की मुहर सहित

वित्तीय नियम संग्रह खण्ड–5, भाग–2 कोषागार प्रपत्र–209 (1)

प्रपत्र संख्या–43 ए (1)

(प्रस्तर 417 एवं 478 देखिए)

धनराशि जमा करने का चालान फार्म

उपकोषागार/बैंक का नाम व शाखा: स्टेट बैंक देवरिया

1. जिस व्यक्ति (पदनाम यदि आवश्यक हो) या संस्था के नाम से धनराशि जमा की जा रही है उसका नाम: शिवम इण्टर उद्योग व्यावसायिक

2. पता: लद्दुकुलवा, देवरिया पो० केवटा ग्राम [illegible]

3. पंजीकरण संख्या/पक्ष का नाम व वाद संख्या (यदि आवश्यक हो)

4. जमा की जा रही धनराशि का पूर्ण विवरण (धनराशि किस हेतु जमा की जमा की जा रही है तथा किस विभाग के पक्ष में जमा की जा रही है।): 17 पा० प० वर्ष–2016–17

5. चालान की सकल राशि: आवेदन शुल्क

6. चालान की निबल राशि

7. लेखाशीर्षक का पूर्ण विवरण/लेखाशीर्षक की मुहर :

8. लेखा शीर्षक का 13 डिजिट कोड

मुख्य लेखा शीर्षक	उप मुख्य शीर्षक	लघु शीर्षक	उप शीर्षक	ब्यौरावार शीर्षक	धनराशि (अंकों में)
0853	00	102	00	01	2000.00
					/

धनराशि (शब्दों में) रु० दो हजार रुपये मात्र योग 2000.00

चालान में लेखा शीर्षक की पुष्टि करने वाले विभागीय अधिकारी के हस्ताक्षर मुहर सहित

जमाकर्ता का नाम व हस्ताक्षर

केवल उपकोषागार/बैंक के प्रयोगार्थ

चालान संख्या 37

दिनांक.......................

अंकों में रू०

शब्दों में रू०

भारतीय स्टेट बैंक S.B.I.
शाखा – देवरिया
30 JUN 2017
सरकारी नगद जमा

प्राप्त किया

प्राप्तकर्त्ता के हस्ताक्षर उपकोषागार/बैंक की मुहर सहित

वित्तीय नियम संग्रह खण्ड–5, भाग–2 कोषागार प्रपत्र–209 (1)

प्रपत्र संख्या–43 ए (1)

(प्रस्तर 417 एवं 478 देखिए) Q1630914

धनराशि जमा करने का चालान फार्म

उपकोषागार/बैंक का नाम व शाखा स्टे.ट. बैंक देवरिया

1. जिस व्यक्ति (पदनाम यदि आवश्यक हो) या संस्था के नाम से धनराशि जमा की जा रही है उसका नाम शिवम ईट उद्योग बोलपुर-भीनगार

2. पता लेहुवावा, देवरिया
प्रो० रामकिशोर गुप्ता

3. पंजीकरण संख्या/पक्ष का नाम व वाद संख्या (यदि आवश्यक हो) 17 पाया

4. जमा की जा रही धनराशि का पूर्ण विवरण (धनराशि किस हेतु जमा की जमा की जा रही है तथा किस विभाग के पक्ष में जमा की जा रही है।) वर्ष-2016-17 रायल्टी

5. चालान की सकल राशि

6. चालान की निबल राशि

7. लेखाशीर्षक का पूर्ण विवरण/लेखाशीर्षक की मुहर :

8. लेखा शीर्षक का 13 डिजिट कोड

मुख्य लेखा शीर्षक	उप मुख्य शीर्षक	लघु शीर्षक	उप शीर्षक	ब्यौरावार शीर्षक	धनराशि (अंको में)
0853	00	800	00	01	86130.00
					86130.00

धनराशि (शब्दों में) रु० छियासी हजार एक सौ तीस मात्र

चालान में लेखा शीर्षक की पुष्टि करने वाले विभागीय अधिकारी के हस्ताक्षर मुहर सहित

जमाकर्ता का नाम व हस्ताक्षर रामकिशोर

केवल उपकोषागार/बैंक के प्रयोगार्थ

चालान संख्या

दिनांक........ 35

अंकों में रु० 86130

शब्दों में

भारतीय स्टेट बैंक
शाखा – देवरिया
30 JUN 20
सरकारी

प्राप्त किया

प्राप्तकर्ता के हस्ताक्षर उपकोषागार/बैंक की मुहर सहित

[illegible]

ला परिषद्/क्षेत्र समिति प्रपत्र संख्या–5 [illegible] 17-18

(नियम 41 देखिये)

साइडेड कार्बन पेपर" पर अमिट पेन्सिल से लिखा जायेगा)

द्/जिले के नाम सहित क्षेत्र समिति के नाम का रबड़ स्टाम्प

रसीद संख्या 394023

र संख्या [illegible]

श्रीमती [illegible] से

रु० [illegible]

के मद्दे प्राप्त हुआ।

रुपया 10,505—

मुख्य अधिकारी/खंड विकास अधिकारी

22-3-18

कर-समाहर्त्ता (जिला कलेक्टर)

रोकड़िया

23-3-18

माँग तथा वसूली के अतिरिक्त कर अधिकारी।

[illegible] 13.9.2017-5000 पुस्त [illegible]

जिला परिषद्/जिले के नाम सहित क्षेत्र समिति के नाम का रबड़ स्टाम्प

वही संख्या

रसीद संख्या 394023

रसीद के अनुसार भुगतानकर्त्ता का नाम

रसीद के अनुसार उससे वसूल की गई धनराशि

रसीद के अनुसार किस मद्दे वसूल की गई

रसीद के अनुसार कर-समाहर्त्ता का नाम, जिसने धनराशि वसूल की

इस कूपन को जमा करने वाले अधिकारी का नाम तथा पदनाम

2016-17

परिषद्/क्षेत्र समिति प्रपत्र संख्या 5

(नियम 41 देखिये)

डेढ़ कार्बन पेपर पर अमिट पेन्सिल से लिखा जायेगा)

जिले के नाम सहित क्षेत्र समिति के नाम का रबड़ स्टाम्प

रसीद संख्या 269560

संख्या ________ से

________ (रुपया शब्दों में)

________ के पूर्ण/आंशिक भुगतान

________ के मद्दे प्राप्त हुए।

— रुपया

मुख्य आयकल्प/खंड विकास अधिकारी

____

कर-समाहर्ता (टक्स कलेक्टर)

संख्या

नामित राशि वसूली का प्रभार लिपिक
पद अधिकारी

टि–01 जिला प्रेस 25-9-2015–10,000 पुस्तक

जिला परिषद/जिले के नाम सहित क्षेत्र समिति के नाम का रबड़ स्टाम्प

बही संख्या ________ रसीद संख्या ________

269560

रसीद के अनुसार भुगतानकर्ता का नाम ________

रसीद के अनुसार उससे वसूल की गई धनराशि ________

रसीद के अनुसार किस मद्दे वसूल की गई ________

____

रसीद के अनुसार कर-समाहर्त्ता का नाम, जिसने ________

धनराशि वसूल की ________

इस कूपन को जमा करने वाले ________

अधिकारी का नाम तथा पदनाम

____

[illegible] शुल्क, 2015-2016

[illegible] 2016-2017/[illegible]
...न परिषद/क्षेत्र समिति प्रपत्र संख्या 3
(नियम [illegible] देखिये) 9-1-16

...कार्बन पेपर पर अंकित (प्रिन्टेड) [illegible] 7355 आदर्श
...व जिले के नाम सहित क्षेत्र समिति के नाम का रबड़ स्टाम्प
[illegible]
रसीद संख्या
...टर संख्या 964175 से
(रुपया शब्दों में)
के पूर्ण/आंशिक भुगतान में
मद्दे प्राप्त हुआ।
रुपया
मुख्य अधिकारी/खंड विकास अधिकारी
4550/—
कर-समाहर्ता (टैक्स कलेक्टर)
रोकड़िया 2-3-16
मांग तथा वसूली का प्रभारी लिपिक
कर अधिकारी।

यू0 पी0–01 जिला पंचायत–25-9-2010–10,000 बुक
पी0/आफसेट)।

जिला परिषद/जिले के नाम सहित क्षेत्र समिति के [illegible] स्टाम्प

...ी संख्या
रसीद संख्या 964175
रसीद के अनुसार भुगतानकर्ता का नाम
रसीद के अनुसार उससे वसूल की गई धनराशि
रसीद के अनुसार किस मद्दे वसूल की गई
रसीद के अनुसार कर-समाहर्ता का नाम, जिसने
धनराशि वसूल की
इस कूपन को जमा करने वाले
अधिकारी का नाम तथा पदनाम

टी०वी०कर वर्ष 2015-2016

जिला परिषद्/क्षेत्र समिति प्रपत्र संख्या 5
(नियम 41 देखिये)

("डबुल साइडेड कार्बन पेपर" पर अमिट पेन्सिल से लिखा जायेगा)

जिला परिषद जिले के नाम सहित क्षेत्र समिति के नाम का रबड़ स्टाम्प

डी संख्या ———— रसीद संख्या 406278

ग रजिस्टर संख्या —— [illegible] से

———— (रुपया शब्दों में)

ल संख्या —— [illegible] पूर्ण/आंशिक भुगतान

—— [illegible] छः हजार रुपये मात्र

———— रुपया

मुख्य अधिकारी/खंड विकास अधिकारी

थान ————

नांक ———— 6000/—

कर समाहर्त्ता (टैक्स कलेक्टर)

[illegible]

कार

मांग तथा वसूली का प्रभारी लिपिक

कर अधिकारी 6-16

एस० यू० पी०–01 जिला पंचायत–25-9-2010–10,000 बुक (डी०पी०/आफसेट)।

00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00
00

————

जिला परिषद्/जिले के नाम सहित क्षेत्र समिति के नाम का रबड़ स्टाम्प

बही संख्या ———— रसीद संख्या 406278

रसीद के अनुसार भुगतानकर्त्ता का नाम ————

रसीद के अनुसार उससे वसूल की गई धनराशि ————

रसीद के अनुसार किस मद्दे वसूल की गई ————

————

रसीद के अनुसार कर-समाहर्त्ता का नाम, जिसने ————

धनराशि वसूल की ————

इस कूपन को जमा करने वाले ————

अधिकारी का नाम तथा पदनाम

————

[illegible] 2011-15

/क्षेत्र समिति प्रपत्र संख्या 5
नियम 41 देखिये)

ंग पेपर' पर अमिट पेन्सिल से लिखा जायेगा)

नाम सहित क्षेत्र समिति के नाम का रबड़ स्टाम्प

रसीद संख्या 708038

प्रो [illegible] से

(रुपया, शब्दों में)

के पूर्ण/आंशिक भुगतान

के मद्दे प्राप्त हुआ।

मुख्य अधिकारी/खंड विकास अधिकारी

कर-समाहर्ता (टैक्स कलेक्टर)

रोकड़िया

मांग तथा वसूली का प्रभारी लिपिक
कर अधिकारी।

जिला पंचायत--25-9-2010--10,000 बुक

जिला परिषद/जिले के नाम सहित क्षेत्र समिति के नाम का रबड़ स्टाम्प

बही संख्या ______ रसीद संख्या ______

708038

रसीद के अनुसार भुगतानकर्ता का नाम ______

रसीद के अनुसार उससे वसूल की गई धनराशि ______

रसीद के अनुसार किस मद्दे वसूल की गई ______

रसीद के अनुसार कर-समाहर्ता का नाम, जिसने ______

धनराशि वसूल की ______

इस कूपन को जमा करने वाले ______

अधिकारी का नाम तथा पदनाम

सी.पि. [illegible] वर्ष 2014-15

जिला परिषद्/क्षेत्र समिति प्रपत्र संख्या 5
(नियम 41 देखिये)

('डबुल साइडेड कार्बन पेपर' पर [illegible] पेन्सिल से लिखा जायेगा)

[illegible] परिषद् जिले के नाम सहित क्षेत्र समिति के नाम का रबड़ स्टाम्प

ही संख्या ———— रसीद संख्या 134268

ग रजिस्टर संख्या [illegible] से

श्री [illegible]

(रुपया शब्दों में)

बिल संख्या [illegible] के पूर्ण/आंशिक भुगतान के मददे प्राप्त हुआ।

———— रुपया [illegible]

6000=00

मुख्य अधिकारी/खंड विकास अधिकारी

स्थान ————

दिनांक ————

[illegible]

[illegible]

कर-समाहर्ता (टैक्स कलेक्टर)

[illegible] तथा वसूली का प्रभारी [illegible] कर अधिकारी।

टिप्पणी

[illegible] 2010-10 [illegible]

[illegible]

जिला परिषद्/जिले के नाम सहित क्षेत्र समिति के नाम का रबड़ स्टाम्प

बही संख्या ———— रसीद संख्या 134268

रसीद के अनुसार भुगतानकर्ता का नाम ————

रसीद के अनुसार उससे वसूल की गई धनराशि ————

रसीद के अनुसार किस मददे वसूल की गई ————

रसीद के अनुसार कर-समाहर्त्ता का नाम, जिसने ————

धनराशि वसूल की ————

इस कूपन को जमा करने वाले ————

अधिकारी का नाम तथा पदनाम ————
